Integrated Rurban Development and Climate Resilience Project (IRDCRP)

Ministry of Agriculture, Livestock, Lands and Irrigation



Social Screening Report (SSR) and Social Management Plan (SMP) of

Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme, Tissamahara Division, Hambanthota District

(Department of Irrigation)

Social Development Section-IRDCRP
October 19, 2026,

LIST OF ABBREVIATIONS

ID	Department of Irrigation
PID	Provincial Irrigation Department
ASC	Agrarian Service Center
AP	Affected Party
CBO	Community Based Organization
C-EMP	Contractor's Environmental and Social Management Plan
DAD	Department of Agrarian Development
DS	Divisional Secretary
ES	Environmental Section
ESF	Environmental and Social Framework
ESHS	Environmental, Social, Health and Safety
EMP	Environmental and Social Management Plan
ESS	Environmental and Social Standard
FO	Farming Organization
GBV	Gender Based Violation
GN	Grama Niladhari
GoSL	Government of Sri Lanka
GRC	Grievance Redress Committee
GRM	Grievance Redress Mechanism
HH	Household
IP	Indigenous People
IRDCRP	Integrated Rurban Development and Climate Resilience Project
MoALLI	Ministry of Agriculture, Livestock, Lands and Irrigation
NGOs	Non-Government Organizations
OHS	Occupational Health and Safety
PDOs	The Project Development Objectives
PMU	Project Management Unit
PPE	Personal Protective Equipment
SSDS	Senior Social Development Section
SDS	Social Development Section
SEA	Sexual Exploitation and Abuse
SEA	Sexual Exploitation and Abuse
SMP	Social Management Plan
SH	Sexual Harassment
SSDS	Senior Social Development Specialist
SSR	Social Screening Report

WB	World Bank

Table of Contents

01). Introduction..... 5

02). Socio economic demographic background 6

03). Project cognizance: 7

04). Intervention activities:..... 8

05). Existing issues of Farming Community. 8

06). Impact area: 8

17). Land ownership status of the project area. 13

08). Consultations: 14

09). Social Screening..... 14

10). Screening decision on impact categorization:..... 17

11). Recommendations: 17

12). Safeguard Implementation and Monitoring. 17

13). Report preparation: 18

Annex 01: Social Screening Checklist. 19

Annex 02: Consultation Note of Social screening..... 28

Annex 3: Farmer organization meeting minutes 30

Annex 04: Social Management Plan (SMP)..... 37

Annex 05: Individual Code of Conduct (with Sinhala Version) 43

Annex 06: composition of the GRCs...... 51

Annex 07: Legal Framework and World Bank's ESF Policy and Standards 53

Annex 08: Contingency plan..... 54

Annex 10: The List of Beneficiaries 59

.Annex 11: Asset clearance letter of ID..... 61

.Annex 12: BOQs..... 62

1.	Proposed Tender Date	:	
2.	Proposed Work Commencement Date	:	
3.	Contract Value	:	

01). Introduction

The Irrigation Department (ID) in Sri Lanka plays a key role in promoting sustainable agriculture and safeguarding farmers' interests through irrigation management, paddy land regulation, agrarian reforms, and support services like credit and extension. Under the Integrated Rurban Development and Climate Resilience Project (IRDCRP), Subcomponent 2.2 focuses on improving irrigation systems. In the Hambanthota District, the Irrigation Department (ID) plans Rehabilitation of Distribution Canal System under the Irrigation and Water Resources Management Program of track 01, 02, & 03 in Left Bank Main Canal (LBMC) in Lunugamwehera Scheme, Thisamaharama Division, Hambanthota Range. ID will handle project design, implementation, and quality control, while the PMU oversees supervision, monitoring, evaluation, and payments. Once completed, ID will manage operations and maintenance, with active participation from the farming community and stakeholders such as local government officials, and community-based organizations (CBO) through mechanisms like the Social Audit Committee (SAC) and Grievance Redress Mechanism (GRM).

The primary objective of restoring this canal network is to improve water management and boost overall agricultural productivity. During the site visit, the safeguard team observed heavy water loss caused by seepage and leaks. Once the rehabilitation of DCs under LBMC is completed, the Irrigation Department (ID) expects to save enough water to cultivate an additional 2,500 acres while fully meeting the water requirements of existing paddy fields.

Map 1: Project Area – DC 01 Rehabilitation Sites

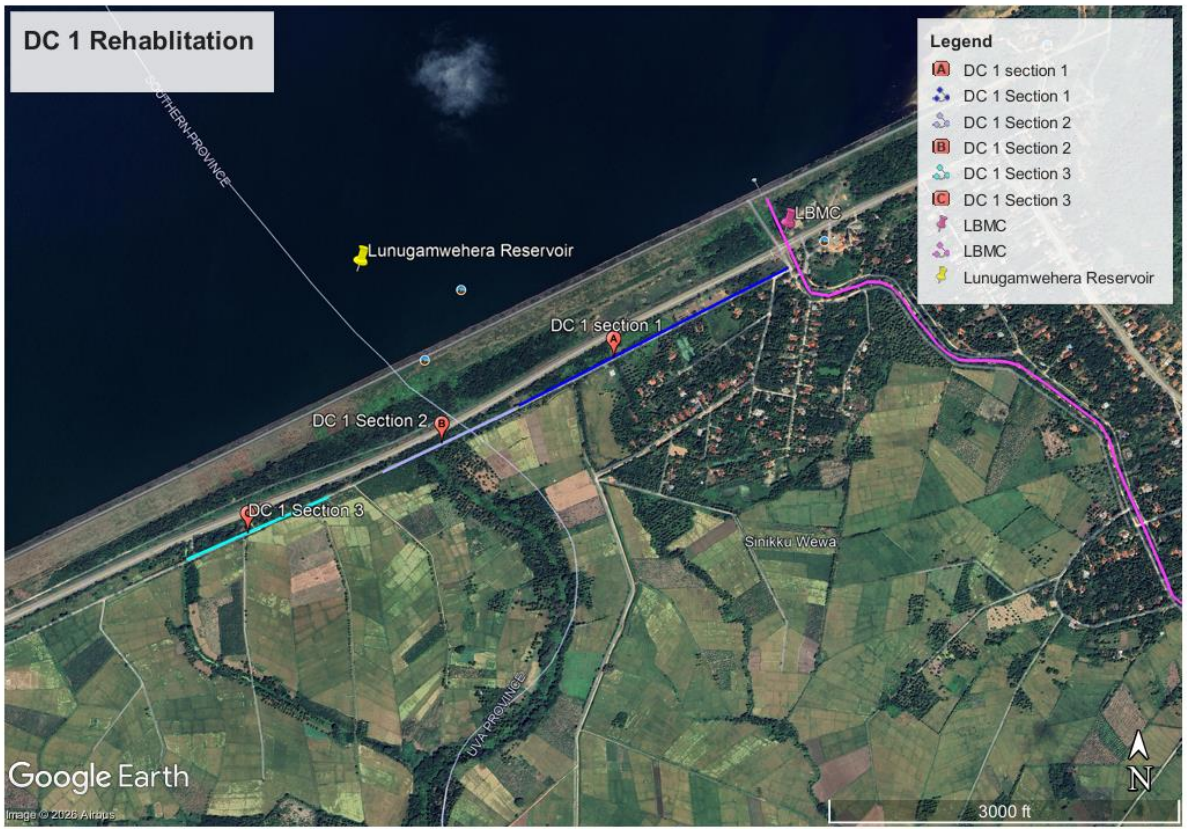

Source: Google Earth

The each tracks consist of several distribution canals (DCs) and field canals (FCs). The sub project is part DC 1 of track 01, LBMC. For technical reasons, the ID has divided DC 1 into three main sections as follows.

Table 1: Subproject division of DC 1

No	Track No.	DC No.	Canal Section	Length
01	01	01	Section 01	From 0+150 to 0+810
02			Section 02	From 0+810 to 1+189
03			Section 03	From 1+320 to 1+781

Table 2: Subproject Location

No	Name of Scheme	Section	GND	Divisional Secretariat	GPS coordinate
01	Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme	From 0+150 to 0+810, from 0+810 to 1+189 & from 1+320 to 1+781	Seenimunna (70)	Lunugamwehera	6°21'50.39"N, 81°13'42.45"E
			Seenukkuwa (50)	Thanamalvila	

02). Socio economic demographic background

The proposed first section of DC 01 (from 0+150 to 0+810) runs through two Grama Niladhari (GN) divisions; Seenimuna GN division and Seenukkuwa GN division. The Seenimuna GN division is in the Lunugamwehera DS division of Hambantota District, and the Seenukkuwa GN division falls under the Thanamalvila DS division of Monaragala District. The second and third sections of the DC 01 run entirely through the Senimunna GN division.

The following tables depict the demographic data for both GN divisions.

***Table 3:** The gender distribution*

DS division	Name of GND	Male	%	Female	%	Total
Lunugamwehera	Seenimunna (70)	543	48.7	573	51.3	1116
Thanamalvila	Seenukkuwa (50)	1035	50.2	1028	49.8	2063
Total		**1578**	**49.6**	**1601**	**50.4**	**3179**

Source: Department of Census & Statistics, 2024

***Table 4:** Age group distribution*

Age Group	0 - 14	%	15 - 59	%	60 - 64	%	65 and above	%	Total
Seenimunna	230	20.6	626	56.1	57	5.1	203	18.2	1116
Seenukkuwa	449	21.8	1113	54	133	6.4	368	17.8	2063
Total	**679**	**21.4**	**1739**	**54.7**	**190**	**6.0**	**571**	**18.0**	**3179**

Source: Department of Census & Statistics, 2024

Table 5: Ethnic distribution

GND Name	GND Code	Sinhalese	%	Other	%	Total
Seenukkuwa	70	2060	99.9	3	0.1	2063
Seenimunna	50	1114	99.8	2	0.2	1116
Total		**3,174**	**100.0**	**5**	**0.3**	**3179**

Source: Department of Census & Statistics, 2024

Table 6: Religious distribution

GND Name	GND Code	Buddhist	%	Other	%	Total
Seenukkuwa	70	2060	99.9	3	0.1	2063
Seenimunna	50	1112	99.6	4	0.4	1116
Total		**3172**	**99.8**	**7**	**0.2**	**3179**

Source: Department of Census & Statistics, 2024

Apart from a small minority belonging to other ethnic and religious groups, the vast majority of the population is Sinhala Buddhist. Local livelihoods rely primarily on paddy cultivation, as well as supplementary crops such as banana and papaya, and animal husbandry etc.

03). Project cognizance:

Following table 01 illustrates project identification information with respect to the proposed project.

Table 7: Project details

1. Project title:	**Rehabilitation of DC 01 of Track 01 LBMC of Lunugamwehera Scheme**
2. Agency of Employer	Integrated Rurban Development and Climate Resilience Project
3. Duration	Three years
4. Estimated total cost	
Section one - From 0+150 to 0+810	Rs 19,455,840.00
Section two - from 0+810 to 1+189	Rs 28,115,860.00
Section Three - from 1+320 to 1+781	Rs 20,355,000.00
5. Project Implementation Agency	Irrigation Department
6. Design and Supervision	Irrigation Department, Lunugamwehera
7. Contact person	Project Director IRDCRP

04). Intervention activities:

Table 8: Project interventions

Name of the Sub Project	Description
Rehabilitation of DC 01 Track 01, LBMC of Lunugamwehera Scheme	1. Converting earthen canals into concrete-lined canals

05). Existing issues of Farming Community.

The absence of concrete-lined canals results in significant water loss from leakage and seepage. This infrastructure deficit leads to inefficient irrigation practices and inequitable water distribution. Consequently, farmers face reduced cultivation areas, lower crop yields, and frequent user conflicts, ultimately undermining regional agricultural productivity and local livelihoods.

06). Impact area:

Site Description, Preventing Crop Damage and Traffic Safety Management

The site is accessible via Lunugamwehera–Kataragama road and left bank main canal (LBMC) road.



Figure 01: The site access

To minimize disruption, major construction activities are scheduled for the off-season. Under standard water management practices, sufficient water will be provided for initial land preparation and mudwork.

Following this, a rotational water supply schedule will be implemented, delivering water for four consecutive days followed by a three-day shutoff.

To ensure a continuous water supply for farming, the contractor must strictly adhere to this schedule and adjust their construction activities accordingly. During the joint site inspection, ID officials informed that necessary clauses will be incorporated into the contract documents to enforce compliance. If required, the contractor must also implement temporary bypass methods to ensure agricultural operations remain unaffected.

The Lunugamwehera–Kataragama Road runs downstream of the Lunugamwehera Reservoir, passing through the reservoir reservation area. The distribution canal scheduled for rehabilitation runs parallel to its service road along the edge of reservoir reservation. Near the canal's starting point, four residential houses are situated downstream of the service road. Because these households do not use the DC 1 service road for access, no significant disruptions to them are anticipated. Although the service road does not lead to any residential driveways, local farmers frequently use it to reach surrounding paddy fields.

Because the road is frequently used, especially for transporting harvests, construction activities must incorporate proper safety measures for both pedestrians and vehicles. Uninterrupted road access must be maintained throughout the construction period, and construction materials must be stockpiled with care. The contractor must display proper warning signage, clearly demarcate material storage locations, install hard barricading near exposed reinforced steel bars, and complete all formwork stripping or backfilling by the end of each workday.

Given the scope and nature of the proposed works, no significant impact on crop yields is anticipated, even if minor construction extends into the active cultivation season. Table No 8 outlines the extent of paddy lands served by these canals and the associated livelihood opportunities.

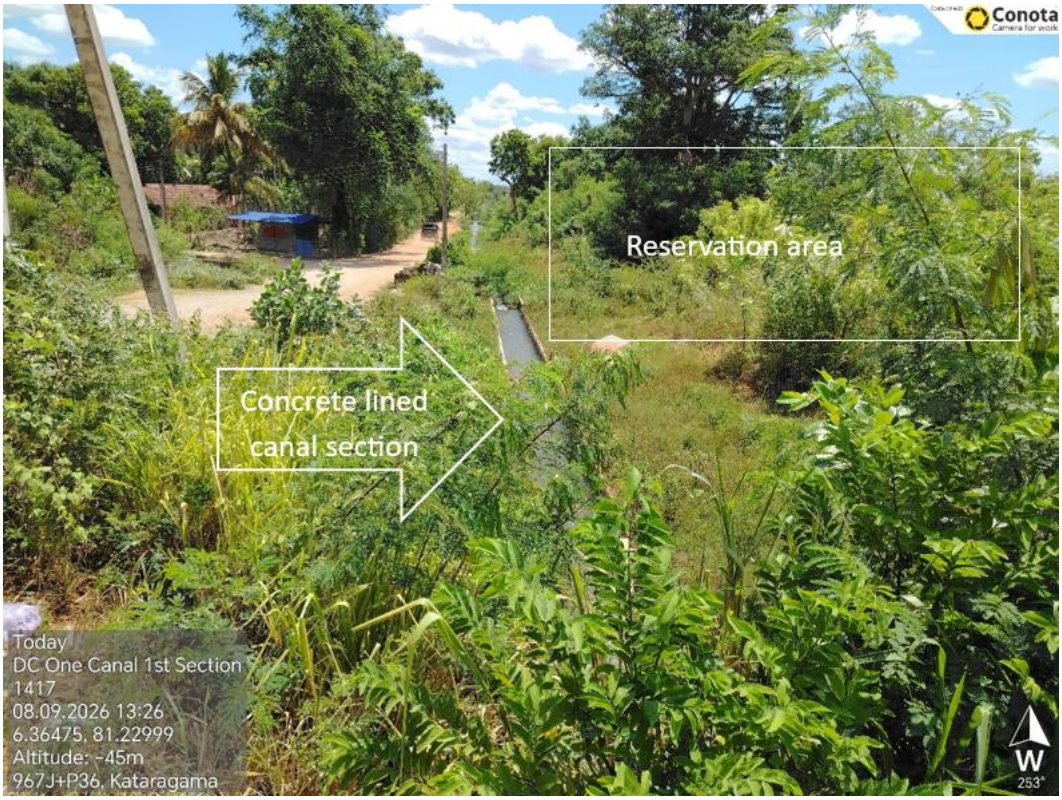

Starting Point of DC 1 and Surrounding Environment



Unlined Canal Section Proposed for Concrete Lining



Overgrown Vegetation along the Canal Bank & inside the canal



Existing Concrete-Lined Canal Section



Canal Section Designated for Concrete Lining

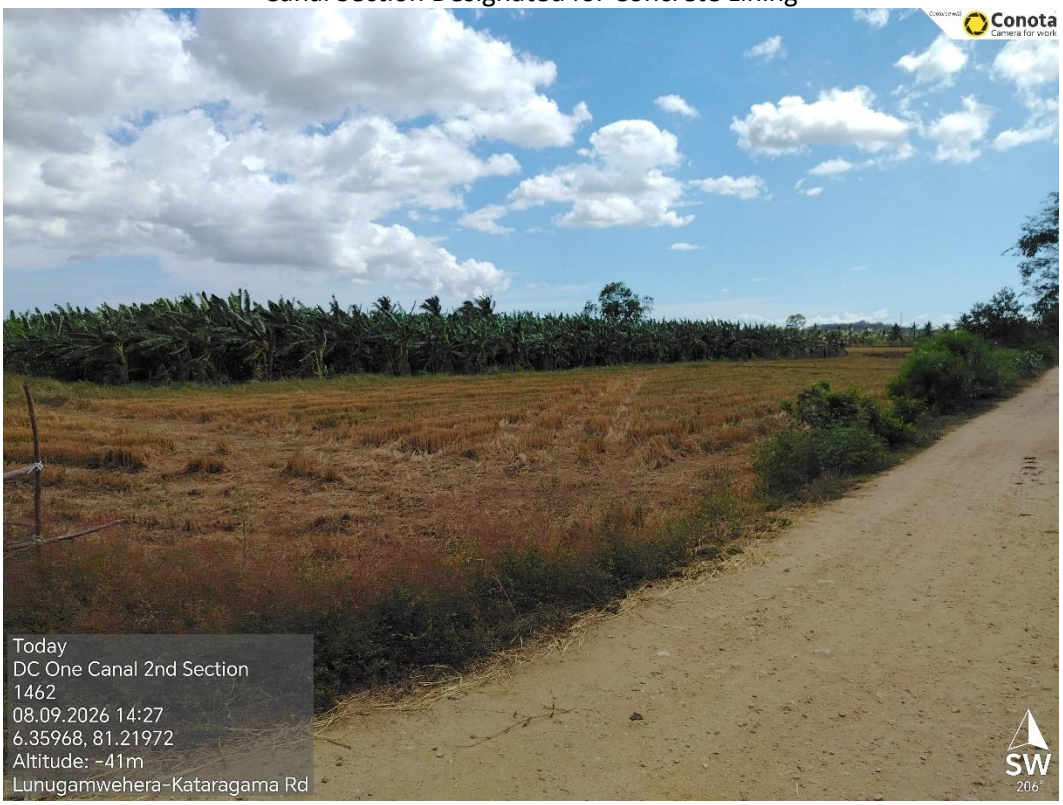

Paddy Fields and Banana Plantations Irrigated by DC 1



Water Loss Caused by Seepage and Bank Leakage

Figure 02: Surrounding environment of the project site

Table 9: The extent of paddy areas belongs to the tank.

Name of the Sub Project	Cultivation	Season	Existing Cultivation			After Rehabilitation		
			Extent (ac)	Extent Harvest (M.T.)	No. of farmers	Extent (ac)	Extent Harvest (M.T.)	No. of farmers
Rehabilitation of DC 01 Track 01 LBMC of Lunugamwehera Scheme, Hambanthota District	Paddy	Maha	100	305	65	113	366	80
		Yala	100	220	65	113	264	80
	Other Field Crops	Maha	90	240	50	90	288	60
		Yala	90	230	50	90	276	60

17). Land ownership status of the project area.

The canal runs parallel to the service road. Because it is bounded upstream by the reservoir reservation and downstream by the service road, no house or agricultural access will be impacted either temporarily or permanently. The canal length and its reservation fall entirely under the ownership of the ID; therefore, no land acquisition is required, and formal clearance from the ID is sufficient for project execution. Consultations and a joint field inspection with the ID and the Farmer Organization (FO) confirmed that

surrounding lands are occupied solely by Land Development Ordinance (LDO) permit holders, with no encroachers identified within the project site.

08). Consultations:

project planning and the social screening to examine the feasibility and importance of the proposed project. The Social Development and Environmental Section of IRDCRP have had consultations with the relevant officials and community leaders of the farming organization. The importance of the project, the nature of the IRDCRP, the proposed project intervention activities, compliance with the Environmental and Social Framework (ESF), and the Social Audit Committee (SAC) and Grievance Redress Mechanism (GRM) procedures were discussed during the consultation. Further information on this is attached (Annex -1).



Figure 03: Public consultations during the site inspection of DC 1

09). Social Screening

The social screening checklist was completed to identify potential impacts of the project (Annex 1). The key findings are summarized below:

i. Land-Related Impacts

- **Construction Activities:** Physical construction work and rehabilitation of existing facilities will take place, and measures to mitigate social impacts owing to such physical construction and rehabilitation are included in the SMP (Annex-02).

- **Land Acquisition:** No land acquisition or house demolition is required due to the construction site belonging to the ID. The land is free from encumbrances and it is under the implementing agency's control.

- **Settlements Nearby**: A few residential housing units are located near the starting point of DC 1. However, because these houses are accessed via a separate road rather than the DC 1 service road, no significant adverse impacts on nearby private structures or properties are anticipated.

- **Access to Facilities:** The proposed construction activities along the DC 1 service road present several temporary access and safety challenges due to the shared usage of the access road by construction crews, local farmers, and commuters.

  To address potential disruptions to agricultural activities, it is recognized that local farmers frequently rely on the service road to transport seasonal harvests and agricultural supplies. Heavy machinery movement, equipment parking, and active trenching could block this critical access route. To resolve this, the contractor must maintain uninterrupted road access throughout the construction period and assign dedicated traffic controllers to coordinate the safe movement of heavy equipment alongside local vehicles and pedestrians. Whenever feasible, necessary actions shall be taken to divert traffic to alternative routes. Clear warning signage and informational boards must be placed at starting points and key access points, detailing the nature of the work, expected project duration, and alternative travel paths.

  Regarding safety hazards from shared road use, the simultaneous transit of machinery, pedestrians, and agricultural traffic creates a high risk of collisions and injuries. To mitigate these risks, the contractor is required to install proper warning signage and clear directional markers ahead of active work zones. Additionally, rigid hard barricading must be erected around high-risk areas, particularly near open excavations and exposed reinforced steel bars.

  In terms of material management and roadway obstruction, random or improper stockpiling of construction materials and excavated soil along the service road reduces roadway capacity and risks obstructing secondary access paths used by nearby residents. To prevent this, material stockpiling must be strictly restricted to designated, clearly demarcated storage zones located off the main access path, and material placement near residential access routes or active driveways must be prohibited.

  Finally, to address overnight hazards posed by ongoing work, incomplete structural components, surplus formwork, or open trenches left unattended after hours present severe risks to evening and early morning commuters. The contractor must enforce mandatory daily site cleanup routines, ensuring that all formwork stripping, trench backfilling, or temporary trench covering is fully completed by the end of each workday.

ii. Dam and Irrigation-Related Impacts

- N/A

iii. Livelihood Impacts: The proposed construction schedule and water distribution plan along the canal system present temporary livelihood and agricultural challenges for local farming communities.

To minimize risks to agricultural yield, local farming relies heavily on a predictable water supply during cultivation. Unexpected water cuts, extended shutoffs beyond three days, or delays during initial land preparation could disrupt planting cycles and damage crops. To prevent this, major construction work will be scheduled during the off-season, and standard water management practices will ensure adequate water for initial land preparation and mudwork. Additionally, the contractor must follow the agreed rotational schedule (four days of water supply followed by three days of shutoff) and plan their construction activities around these supply periods.

To ensure strict compliance and protect farming operations, Irrigation Department (ID) officials will include binding clauses in the construction contract. If construction physically obstructs the canal, the contractor must set up temporary bypass channels or pipes to keep water flowing and ensure local farming remains uninterrupted.

iv. Labour Related Impacts

- Priority will be given to local hiring, especially FO members. External workers may also be brought in and managed through the Code of Conduct and SMP guidelines. Labour camps will be erected with appropriate mitigation measures. Conduct awareness programs for the labour force on hygiene and the dangers of STD/HIV/AIDS/OHS.

v. Gender and Social Issues

- Gender-related awareness programs are planned. Also, it will ensure that no gender-based violence (GBV) issues are occurred during implementation of the project.

vi. Community Contribution and Engagement

- Farmer Organizations (FOs) and CBOs will be mobilized for grievance redress mechanisms and social audits committee (SAC) including CMC process. Beneficiaries will contribute to certain collective activities and monitoring processes. The counterpart contribution will be evaluated and documented after project completion.

vii. Minority and Indigenous Impacts

- The project does not affect ethnic minority groups or indigenous populations.

viii. Labour Safety & Site Protocols

The area is frequented by snakes. specialized protocols are mandatory to safeguard the workforce.

- Morning safety toolboxes must cover awareness regarding venomous snakes
- High-ankle safety boots (or snake guards) and heavy-duty gloves are mandatory for all workers handling cleared brush or moving construction materials.
- Site supervisors must be certified in basic snakebite management (keeping the patient immobilized; no cutting or suctioning). Fully stocked first-aid kits with pressure bandages must be maintained on-site. A dedicated rescue vehicle must remain on standby near site at all times during working hours.

10). Screening decision on impact categorization:

Once reviewing the key findings, it is determined that the project can be categorized as a low-impact/no-impact safeguard category, and further explanation is included in Annex 01.

11). Recommendations:

Once reviewing the above screening, it can be recommended to implement the following mitigation measures that need to be fulfilled before commencing construction of the project for addressing possible social impacts.

i. Social Management Plan (SMP).

In adhering to WB procedures, the SDS-IRDCRP committed to making a Social Management Plan to mitigate social-related possible impacts during the implementation of the sub-project (Annex 02). This SMP shall be included in the bidding documents as a separate plan (as a part of EMP).

ii. Individual Codes of Conduct for the contractor:

Individual Codes of Conduct for the contractor have been made and included as attachment in the SMP in order to sign an agreement with the contractor to ensure implementing environmental, social, health, and safety (ESHS), occupational health and safety (OHS) standards, sexual exploitation and abuse (SEA), sexual harassment (SH), and preventing gender-based violence (GBV). The contractor shall adhere to reporting through the GRM or to his manager any suspected or actual GBV by a fellow worker, whether employed by his company or not, or any breaches of this Code of Conduct (Annex 03).

iii. Grievance Redress Mechanism (GRM

The SDS-IRDCRP has planned to establish a three-tier Grievance Redress Mechanism (GRM) for the aforesaid sub project. Accordingly, a site-level Grievance Redress Committee (GRC) will be formed to address possible social issues (see the annex 04).

iv. Conducting Safeguard Training:

The SDS and ES (IRDCRP) committed to conducting relevant safeguard training to enhance the knowledge of the technical staff members in order to ensure the World Bank's social safeguard compliance when commencing construction work on the proposed sub-projects.

12). Safeguard Implementation and Monitoring.

Site-level GRC will be established to reduce the incidence of extensive and time-consuming issues involving minor issues. The Safeguard Officer (SO)/Project Manager (PM)/Site Supervisor of the contractor assigned to the project will be responsible for handling the possible grievance and social issues at the field level. EMP will be included in the bidding documents, and there will be a budget allocated in the contract for EMP implementation. Representatives of ID should monitor safeguard issues proactively at the construction site with communicating PMU-IRDCRP. As well, the Social Audit Committee (SAC) will be formed to help monitor the quality of civil works, monitor impacts to the community, and support the

operation of the GRM. The Social Development Officer of IRDCRP will overall facilitate the follow-up of site-level social safeguard functions, and under the facilitation of administration, the IRDCRP Senior Social Development Specialist is responsible for monitoring the social safeguard implementation process.

13). Report preparation:

Name	Designation	Date	Signature
JMAS Bandara	**Consultant for Social Safeguard Management**	**October 19, 2026**	

Annex 01: Social Screening Checklist.

Social Screening Checklist for Potential Sub Projects-IRDCRP

Social Development Section

Ministry of Agriculture, Livestock, Lands and Irrigation

1. Name of Sub-Project: Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme
2. District: Hambanthota
3. Divisional Secretariat: Lunugamwehera
4. Name of the cascade: N/A
5. Relevant Implementing Agency: Irrigation Department
6. GND: Seenimunna (70) & Seenukkuwa (50)
7. Name of the Farming Organization: Lunugamwehera LBMC Track 01, DC 01 Didula Farmer's Organization
8. Agrarian Service Center (ASC)/Divisional Irrigation Office: Irrigation Department - Lunugamwehera
9. GPS Coordination:

No	Name of the Sub Project	GND's	Divisional secretariat	GPS Coordinate
1	Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme	Seenimunna (70) & Seenukkuwa (50)	Lunugamwehera	6°21'50.39"N, 81°13'42.45"E

10. Size/Scale: NCB
11. Description of Project Surroundings (Land Use): The surrounding area consists of paddy fields, banana plantations, a few scattered residential units, the Lunugamwehera–Kataragama Road, and the Lunugamwehera Reservoir and its reservation area.
12. Number of beneficiaries:

Name of the Sub Project	Direct	Indirect	Total
Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme	77	9	86

13. Demographic information of the Seenimunna (70) & Seenukkuwa (50) GN divisions.

The gender distribution

DS division	Name of GND	Male	%	Female	%	Total
Lunugamwehera	Seenimunna (70)	543	48.7	573	51.3	1116
Thanamalvila	Seenukkuwa (50)	1035	50.2	1028	49.8	2063
Total		**1578**	**49.6**	**1601**	**50.4**	**3179**

Source: Department of census & statistics, 2024

Age group distribution

Age Group	0 - 14	%	15 - 59	%	60 - 64	%	65 and above	%	Total
Seenimunna	230	20.6	626	56.1	57	5.1	203	18.2	1116
Seenukkuwa	449	21.8	1113	54	133	6.4	368	17.8	2063
Total	**679**	**21.4**	**1739**	**54.7**	**190**	**6.0**	**571**	**18.0**	**3179**

Source: Department of Census & Statistics, 2024

Ethnic distribution

GND Name	GND Code	Sinhalese	%	Other	%	Total
Seenukkuwa	70	2060	99.9	3	0.1	2063
Seenimunna	50	1114	99.8	2	0.2	1116
Total		**3,174**	**100.0**	**5**	**0.3**	**3179**

Source: Department of Census & Statistics, 2024

Religious distribution

GND Name	GND Code	Buddhist	%	Other	%	Total
Seenukkuwa	70	2060	99.9	3	0.1	2063
Seenimunna	50	1112	99.6	4	0.4	1116
Total		**3172**	**99.8**	**7**	**0.2**	**3179**

Source: Department of Census & Statistics, 2024

14. What are the main sources of livelihoods in the area? Paddy farming, banana cultivation & additional crop cultivations
15. What livelihood opportunities are associated with the existing and enhanced facilities of the sub-project?.

The extent of paddy areas belongs to the tank.

Name of the Sub Project	Cultivation	Season	Existing Cultivation			After Rehabilitation		
			Extent (ac)	Extent Harvest (M.T.)	No. of farmers	Extent (ac)	Extent Harvest (M.T.)	No. of farmers
Rehabilitation of DC 01 Track 01 LBMC of Lunugamwehera Scheme, Hambanthota District	Paddy	Maha	100	305	65	113	366	80
		Yala	100	220	65	113	264	80
	Other Field Crops	Maha	90	240	50	90	288	60
		Yala	90	230	50	90	276	60

16. Are there existing settlements or social sensitive locations near the project area? No. there are 6 residential units beyond the immediate influence area.

17. "If yes" fill the following table:

SN	Social Sensitive Locations	Distance from proposed project site (m)	Description
1	Human settlements	Within 50m buffer zone	Not anticipated significant direct or indirect impact since no house from the access service road adjacent to the DC 1
2	School	-	
3	Hospital	-	
4	Temple	-	
5	Church	-	
6	Kovil	-	
7	Public Gathering location (please specify……)	-	
8	Other	-	

18. **Potential social Impacts from the Sub-Project:**

Social Screening Check List (Potential Impacts from the Sub-Project):

SN	Probable involuntary resettlement impacts	Yes	No	Not Known	Details
Land-Related Impacts					
1	Will the sub project include any physical construction work?	Yes			Concrete lining of the earthen section of the DC 1. (The mitigations are included in SMP.)
2	Does the intervention include upgrading or rehabilitation of existing physical facilities?	Yes			Do

3	Does the project require land acquisition or land related impacts for development (public or private, temporary or permanent)?		No		
4	Does the project cause house demolition (including operating and non-operating ones) due to development?		No		
5	Is the sub project likely to cause partially or fully damage to, or loss of housing, shops, or other resource use?		No		
6	Is the site chosen for this work free from encumbrances and is in possession of the implementing agency?	Yes			The project area is free from encumbrance and it is fully under the jurisdiction of ID.
7	If any land required for the work is privately owned, will this be purchased or obtained through voluntary donation?				Not applicable
8	If the Land parcel has to be acquired, is the actual plot size and ownership status known?				Not applicable
9	Whether the affected land owners likely to lose more than 10% of their land/structure area because of donation?				Not applicable
10	Will the affected land/structure owners likely to lose less than 10% of their land/structures area?				Not applicable
11	Does the urban local body have its own procedures for land acquisition?				Not applicable
12	Will there be any impacts on cultural, community properties or facilities?		No		
13	Are there existing settlements or social sensitive locations near the project area?	Yes			Six residential units are located within the 50m buffer zone. However, these houses have separate access routes and do not rely on the DC 1 service road. Consequently, no significant impacts on these residences are anticipated due to the canal rehabilitation.
14	Is land for material mobilization or transport for the civil work available within the identified work site / Right of way?	Yes			Sufficient land is available within the designated work site / Right of way (ROW) for material mobilization and transport. However, the

					contractor must strictly adhere to the guidelines stipulated in the SSR and EMP.
15	Does the proposed improvement disturb the access to residential areas, or public spaces?		No		To avoid / minimize potential access disruptions to surrounding agricultural lands, the contractor must strictly adhere to the access management guidelines stipulated in the SSR and EMP.
16	Does the proposed improvement disturb the access to residential areas, or public spaces?		No		
17	Are there any other development activities linked to the proposed sub project?		No		
Rehabilitation of dam head works and rip rap associated irrigation infrastructure related impacts					
18	Will improvements to tank bund including the head works and rip rap structures require the water level in the reservoir to be artificially drawn down?		No		Construction activities are limited to canal rehabilitations.
19	Will intervention require temporary suspension of water issuance for irrigation in the canal? (Diminishing water for downstream water uses such as bathing, drinking water supplies, irrigation of home gardens, etc.).		No		Major rehabilitation works are scheduled for the off-season. Additionally, the contractor must align construction with the standard rotational water supply schedule (four consecutive days of water delivery followed by a three-day shutoff). Relevant binding clauses will be incorporated into the contract agreements to enforce compliance. Consequently, no disruptions or changes to the regular irrigation water supply schedule are anticipated.
20	Will there be changes to original design levels of the head works that will result in		No		Construction activities are limited to canal rehabilitations.

	inundation of new land in the catchment?				
21	Will the rehabilitated scheme serve new areas of paddy under its command?		No		Once the full LBMC rehabilitation project is completed, the Irrigation Department (ID) expects to save enough water to cultivate an additional 2,500 acres while fully meeting the water requirements of existing paddy fields.
22	Are there bathing spots that will be unusable during the construction period?	Yes			Construction at specific canal locations may temporarily disrupt access to certain bathing spots. However, suitable alternative bathing locations are available nearby in the immediate vicinity.
23	Are there drinking water supply sources located in the project are that may be rendered unusable during construction period?		No		Canal water is not used for drinking purposes.
Livelihoods Related Impacts					
24	Are there any non-titled people (Squatters) who are living/ or doing business who may be partially or fully affected because of the civil works?		No		
25	Will there be damage to agricultural lands, standing crops, trees, etc.		No		
26	Are there tourism activities taking place in the project area that will get disturbed by construction activity?		No		
27	Due to Rehabilitation activity, will there be damage to agricultural lands, standing crops and other?		No		
28	Will there be any permanent or temporary loss of income and livelihoods as a result of the civil works (Paddy, fisheries activities etc.)? If so for what period?		No		
29	If there are livelihood impacts, have these people/businesses who may suffer temporary loss of incomes or livelihoods		No		There are no livelihood impacts due to rehabilitation of canals.

	been surveyed and identified for any livelihood assistance?				But IRDCRP is planned to assist with skill development programs for farmers (especially considering female groups) and provide opportunities to hire workers from the local workforce.
30	Will people permanently or temporarily lose access to facilities, services, livelihood or natural resources?		No		Temporary access difficulties during construction will be effectively mitigated through the strict implementation of guidelines stipulated in the SSR and EMP.
31	Are there any vulnerable households affected?		No		
32	Does the project cause unemployment?		No		Construction is scheduled during the dry season to prevent disruptions to ongoing agricultural and livelihood activities. Additionally, the project is anticipated to create local employment opportunities during the construction phase.
33	Will there be any other temporary impacts? please describe		No		
Labour Influx Related Impacts					
34	How many workers will be needed for the sub-project, with what skill set, and for what period?				15 approximately
35	Can the project hire workers (skilled and unskilled) from the local workforce?	Yes			Priority for FO members.
36	Will there be workers brought in from outside?	Yes			Labour management will proceed with implementing Code of Conduct.
37	Will a camp be required to house these incoming workers?	Yes			If the contractor cannot hire local labors, camps should be established to maintain a safe distance from residential units & public gathering places.

38	Will the incoming workers be from a similar socio-economic, cultural, religious or demographic background?				The contractor will prioritize hiring local labor whenever available. However, if qualified local workers are not available, external labor may be recruited. To ensure these workers align with local norms and minimize social impacts, all personnel will be required to sign and abide by an Individual Code of Conduct
39	Given the characteristics of the local community, are there any adverse impacts, like OHS-related or community safety issues, that may be anticipated?		No		Mitigation measures have been included in SMP to mitigate possible OHS and community safety-related social issues.
Gender Based Violence/Gender related social issues					
40	Undertaken consultations with women's groups?	Yes			Important gender-related awareness programs have planned to be done.
41	Issues related to GBV and GBV-related concerns about the project have arisen in the community engagement discussions?		No		
42	Is the project construction near school route or other pedestrian access that women and girls use for their daily activities?		No		
Counterpart contribution from the beneficiary community					
43	Will the project mobilize the CBOs, FO, host community for GRM/Social Audit Committee/ etc. activities? If yes, are they need training?	Yes			SDS-IRDCRP has planned to conduct several mobilization programs.
44	Will the project expect any counterpart contribution (CC)from the beneficiary households? (If yes, have you planned to calculate particular contribution)	Yes			Beneficiary farmers will actively participate in certain collective activities outside the project scope. Community monitoring will be conducted by the farmers throughout the process. Once the rehabilitation activities are completed, the

					counterpart contribution (CC) will be evaluated and documented. (Relevant indicators have already been identified in the project monitoring process to measure the CC)
Adverse impacts for Minorities					
45	Whether the project has affected ethnic minority communities and population (If yes, mention)		No		
46	Will there be any permanent or temporary impacts for Indigenous peoples?		No		
47	If yes, fill the specific social screening check list which made for (IP) Waddas community.				Not applicable

19. Screening decision on impact categorization:

Once reviewing the answers above, it is determined that the sub-project will have:

High impacts/ substantial impact	Moderate impacts	Low impacts/No impacts
		Low impacts

Justification:

This project does not require land acquisition for development (public or private, temporary or permanent), and there are no heavy damages to private or public property, dam- and irrigation-related impacts, adverse livelihood impacts, gender and social issues, or minority and indigenous impacts due to the construction of the project. But it can raise possible unforeseen adverse impacts during the construction, which can be managed by GRM, SMP/EMP. Therefore, it can be categorized as a Low impact for social safeguards.

20. The screening was carried out by

JMAS Bandara
(Consultant for Social Safeguard Management -IRDCRP) October 19, 2026

(Name and the designation of the Officer) **(Signature)** **(Date)**

Annex 02: Consultation Note of Social screening

Consultation Note

1. Date: 08.09.2026
2. Venue: DC 01 of Track 01, LBMC of Lunugamwehera Scheme
3. Name of project: Rehabilitation of DC 01 of Track 01, LBMC of Lunugamwehera Scheme, Tissamahara Division, Hambanthota District
4. Details of Participants:

No	Name	Designation/Organization
01	Mr. Janaka	Engineering Assistant (Irrigation)- ID
02	Mr. B.G.S. Muthukumarana	President Didula FO.
03	Mr. W. Ranjith	Secretary Didula FO.
04	Mr. S.P. Kulathunga	Treasury Didula FO.
05	Mr. R. Maduranga	Member
06	Mr. P.M. Wimalasena	Member
07	Mr. R. Ajith	Member
08	Mr. S. Chandrasena	Member
09	Mr.R. Sasintha Madumal	Member
10	Mr. W.S. Pradeep Samantha	Member
11	Mr. L.H. Darmasena	Member
12	Mr. H.E. Wijesooriya	Member
13	Mr. E.W. Kapila	Member
14	Mr. U. Sunil Maithripala	Consultant for Environmental Safeguards Management
15	Mr. J.M.A.S Bandara	Consultant for Social Safeguards Management

Summary of participants

Male	Female	Total
15	00	15

Community feedback and consent	Project Responses / Decision taken (Negotiated)
In response to the request made by the Didula farmer organization of DC 01 of Track 01, LBMC of Lunugamwehera Scheme, the IRDCRP social and environmental team, together with representatives from the ID, carried out a joint field inspection on September 08, 2026. -Community leaders and chairmen of the farming organization met and held deep discussion while observing proposed rehabilitation intervention.	The social and environmental team of IRDCR got comprehensive evidence-based experience regarding the Importance of the proposed canal rehabilitation activities. Hence, the safeguard team decided to make a SMP/EMP, a code of conduct, and a GRM, etc., for the rehabilitation of DC 01 of Track 01, LBMC of

-Members of FO, ID explained the requirement of Rehabilitation of DC 01 of Track 01, LBMC in order to facilitate water supply to paddy cultivation. In this moment discussed, the current issues faced by the farmers are due to the lack of rehabilitation of the tank. As well, following matters discussed. • Disturbance and inconvenience due to construction period. • Safety concerns of the workers • Feasibility of a land location for stockpiling material, • Environmental and social screening and determine the feasibility of the proposed canal rehabilitations. • Managing disturbance to paddy cultivation • Mitigation measures for possible social impacts. In this consultation, the safeguard team identified that there are no significant adverse impacts when rehabilitating the canals. They were satisfied with the mitigation measures proposed to do civil works during the dry season without affecting their cultivation season/livelihoods. As well, they agreed to form a Social Audit Committee (SAC) and facilitate GRM to support the monitoring of civil works, possible social issues, and safeguard activities.	Lunugamwehera Scheme as a priority project. Safeguard team of IRDCRP intervention to facilitate ID to address possible social issues. ID is responsible for ensuring safety matters. The technical staff of the ID coordinates all of the sub-project activities.

Attendance list

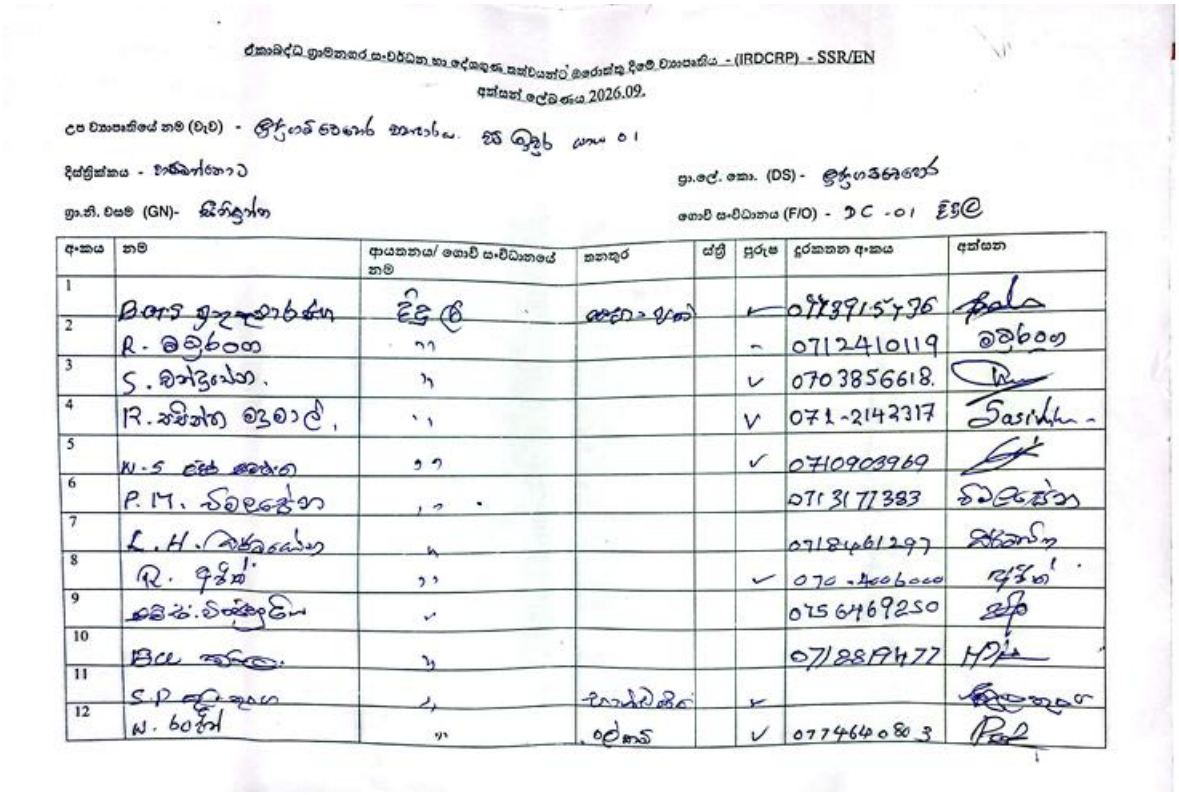

ලියාපදිංචි ග්‍රාමීනකර සංවර්ධන හා රේකලන සක්වයන්ට මරොස්කු දීමේ ව්‍යාපෘතිය - (IRDCRP) - SSR/EN

අත්සන් ලේඛණය 2026.09.

උප ව්‍යාපෘතියේ නම (වැව) - ලුණුගම් වෙහෙර කෘෂිකාර්මික සමූහ ගොවි සංවිධානය 01

දිස්ත්‍රික්කය - මොණරාගල

ප්‍රා.ලේ. කොට්ඨාසය (DS) - සිත්තමගම

ග්‍රා.නි. වසම (GN)- කිරිබත්ගොඩ

ගොවි සංවිධානය (F/O) - LBC-01 වැව

අංකය	නම	ආයතනය/ ගොවි සංවිධානයේ නම	තනතුර	ස්ත්‍රී	පුරුෂ	දුරකතන අංකය	අත්සන
1	[illegible]	වැව	සභාපති		✓	0773915776	[signature]
2	R. මල්ලිකා	〃			-	0712410119	මල්ලිකා
3	S. විජේසේකර.	〃			✓	0703856618.	[signature]
4	R. නිමල්ක මුතුබණ්ඩි.	〃			✓	071-2142317	[signature]
5	W.S. ජයසේන	〃			✓	0710903969	[signature]
6	P.M. විමලසේන	〃				0713177383	විමලසේන
7	L.H. සිරිසේන	〃				0718461297	සිරිසේන
8	R. අමිත්	〃			✓	070-4606000	අමිත්
9	කමිල්. විජේසූරිය	〃				0756469250	කමිල්
10	[illegible]	〃				0718874477	[signature]
11	S.P. අමරසේන	〃	[illegible]		✓		[signature]
12	W. සරත්	〃	ලේකම්		✓	0774640803	[signature]

Annex 3: Farmer organization meeting minutes

Date & Time:	September 15, 2026, at 9:00 AM.
Location:	At the Chairman's residence.
Proceedings:	Started with religious observances, followed by welcoming the officers and farmer members present.
Financial Report Summary	• Previous Balance (as of 2025/11/04): Rs. 129,569.86 • Total Receipts: Rs. 2,208,008.57 (Includes membership fees, development funds, contract payments, loans, and bank interest) • Total Expenses: Rs. 2,051,691.67 (Includes administrative expenses, stationaries, labor costs, contractor payments, transportation, and water bills) • Remaining Bank Balance (as of 2026/09/12): Rs. 156,316.90 • Verdict: The previous meeting minutes (proposed by Indika Weerasinghe, seconded by P.U. Kapil) and the financial report (proposed by R. Wijedasa, seconded by M.A. Gunapala) were formally passed.
Key Discussions & Decisions	**Development & Infrastructure Works:** • Discussions took place regarding the ongoing development work in the area. • A proposal was made to construct a **retaining wall for the DC 01 canal**, as the canal bank has collapsed and is currently posing a risk. • A former Secretary (Mr. H.A. Ananda) noted that canal development work can be carried out smoothly if water flow is managed properly. **Officer & Institutional Inputs:** • The **Agricultural Research Officer** advised farmers to actively get involved and manage the organization's development tasks efficiently. • The **Department of Agrarian Development representative (Diyanthi Jayatilleke)** praised the development work done so far by the Didula Farmers Organization, highlighting that active farmer participation is key to making these projects a success. **Canal Silt Removal Request:** • Members pointed out that **DC 02, FC 02, and FC 03 canals are heavily blocked with silt**, which is severely restricting water flow. • They requested immediate steps to clean and clear these canals.

The meeting concluded with a vote of thanks by the Secretary due to time constraints.

Meeting Minutes

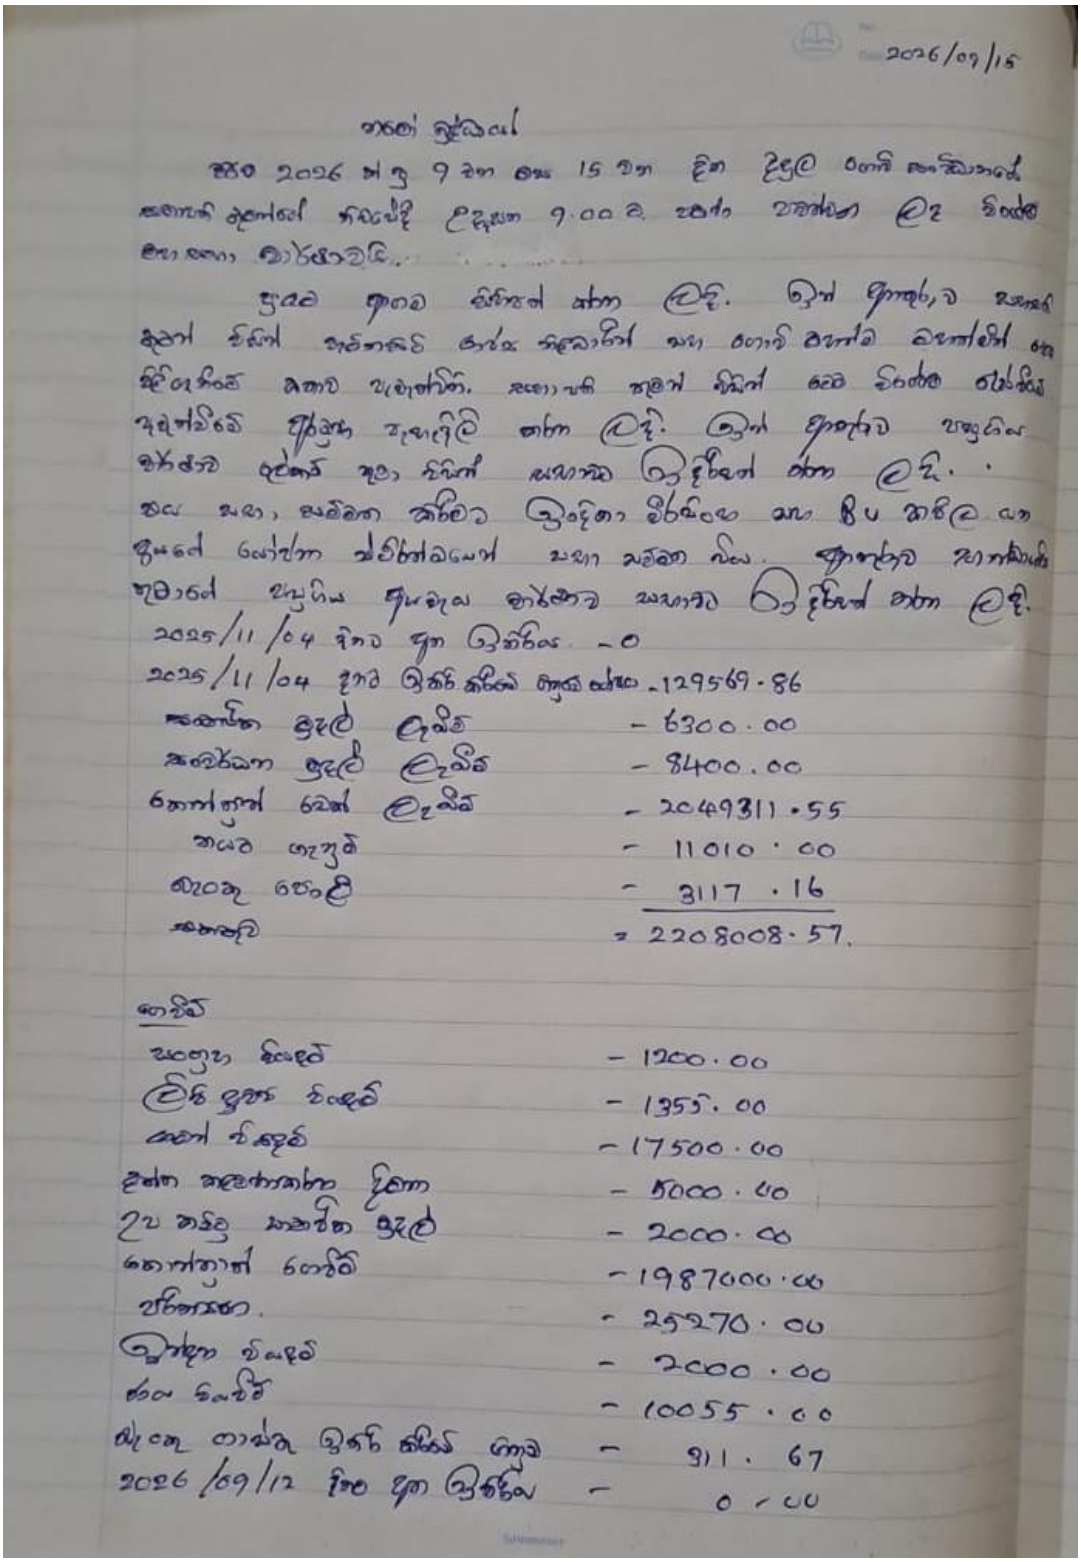

2026/09/15

ආරක්ෂයි!

අද 2026 ක්‌ වූ 9 වන මස 15 වන දින දිඹුලා රජමහා පාසැලේ සභාපති කුලාගේ නිවැරදි උදැසන 9.00 ට පමණ පැමිණෙන ලද මිත්‍රශීල මහතා සහභාගිවිය.

ප්‍රථම රැස්වීම ඇරඹුම් කරන ලදී. ඉන් අනතුරුව සභාපති කුලාගේ මහතා සහ රජාවේ ලේකම් මහත්මිය අතර පැවැත්විණි. සභාවෙහි පළමු රැස්වීම වන බැවින් ඒ පිළිබඳව අවබෝධය ඇතිවීම අරමුණු කරගෙන විවිධ කරුණු සාකච්ඡා කරන ලදී. ඉන් අනතුරුව පහසුවිය අරමුණ කරගත් සභාවේ රැස්වීම් සඳහාත් රැස්වීම් කරන ලදී. එය සඳහා, සම්මත කර්මාන්ත ලැයිස්තුවක් සහ සිය කාර්යය ගැන සිතීමට යන කාලය ගෝලීය ස්වරූපයෙන් සඳහා සම්මත විය. අනතුරුව සාමාජිකයින් අතරින් පහසුවිය අරමුණ කරගත් සභාවේ රැස්වීම් සඳහාත් රැස්වීම් කරන ලදී.

2025/11/04 දිනට අය ඉතිරිය - 0

2025/11/04 දින ඉතිරි කිරීම් ගිණුම් ශේෂය - 129569.86

සාමාජික මුදල් ලැබීම්	- 6300.00
සංවර්ධන මුදල් ලැබීම්	- 8400.00
රජාවෙන් ලබා ලැබීම්	- 2049311.55
පොරොත්තු	- 11010.00
වැටුප් පොළී	- 3117.16
එකතුව	= 2208008.57

වෙනිවී

සඳහන් කිරීමේ	- 1200.00
ලිපි ද්‍රව්‍ය මිලදී	- 1355.00
ලේන් ගීතය	- 17500.00
දින්න කළමනාකාරිත්ව දීමනා	- 5000.00
උප කමිටු සාමාජික මුදල්	- 2000.00
කොන්ත්‍රාත් රෙජිස්ට්	- 1987000.00
පරිණාමය.	- 25270.00
ඉන්ධන මිලදී	- 2000.00
ණය පියවීම්	- 10055.00
බැංකු තාක්ෂණ ගිණුම් ගාස්තු	- 911.67
2026/09/12 දින දින ඉතිරිය	- 0.00

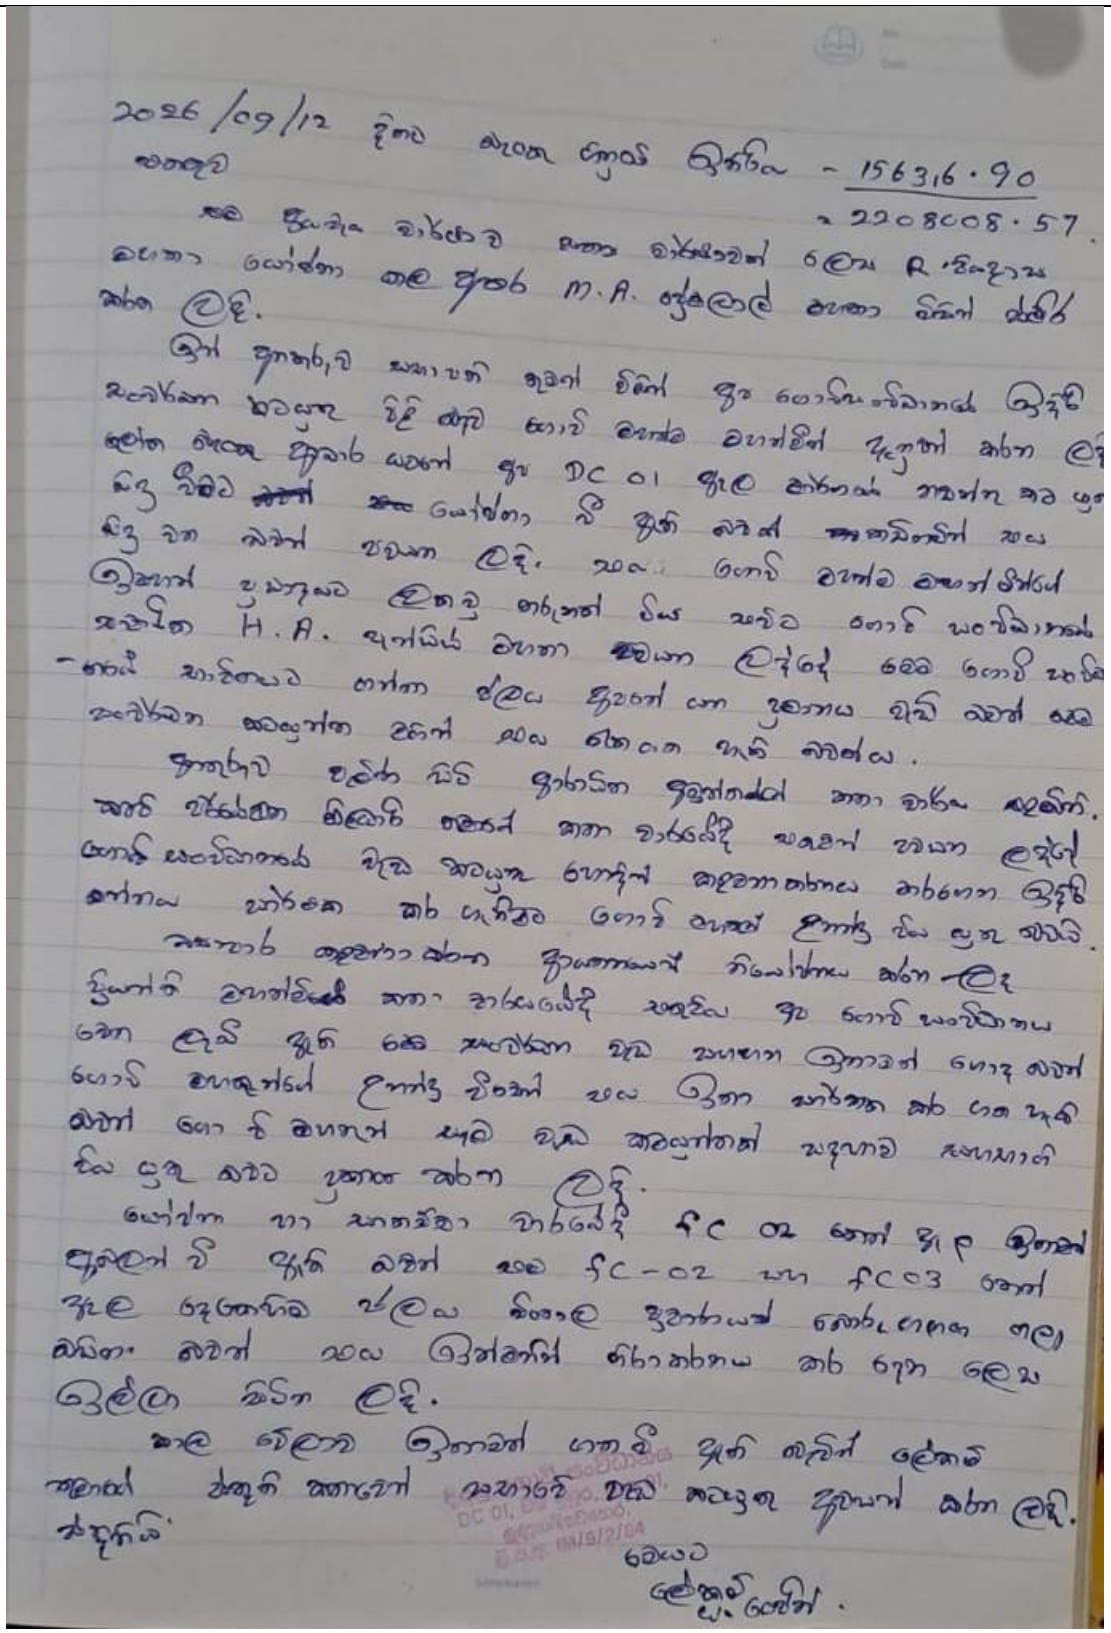

2022/09/12 දිනට අදාල ගණුම් පිළිබඳ - 156316.90
= 2208008.57.
ගණනය

මෙම සියලු වාර්තාව සහ වාර්තාවන් රචනා R. ජිනදාස මහතා විසින් සකස් කර M.A. අල්ලාලේ මහතා විසින් සත්‍යාපිත කරන ලදී.

ඉහත ආකාරයට සහාවෙන් ඉවත් වීමෙන් අප ගොඩනැඟිලිවල සංවර්ධන කටයුතු විදි කළ යුතු බවත් ඒ සඳහා මහජනයාගේ දැනුවත් කරන ලදී. ඉන් අනතුරුව DC 01 අදාළ කාර්යයන් සඳහා අවශ්‍ය කරන ලෙස ගෙවීම් සිදු වන බවත් පැහැදිලි කරන ලදී. සභා ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඉදිරියේදී ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා H.A. ආණ්ඩුව මහතා මෙහෙයවන ලද්දේ එම ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා අවශ්‍ය ප්‍රමාණය ඒ ඒ සභා වෙතින් අය කර ගැනීමට කටයුතු කරන ලදී.

ඉන්පසුව සභාපති විසින් ආරාධිත අමුත්තන්ගේ කතා වාරය ඇරඹුණි. ඒ අනුව ජිනදාස මහතා කතා වාරයේදී සභාවේ ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ සහයෝගය ලබා දෙන ලෙස ඉල්ලා සිටියේය. ඒ සඳහා ඔබ සැමගේ සහයෝගය ලබා දෙන්නේ නම් ඉදිරියේදී ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ දායකත්වය ලබා දීමට කටයුතු කරන බවත් ඒ සඳහා සභාවේ නිලධාරීන් කටයුතු කරන බවත් සඳහන් කළේය.

ඉන්පසුව මහජන සම්බන්ධතා නිලධාරිනිය විසින් කතා වාරය ඇරඹුණි. ඒ අනුව ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ දායකත්වය ලබා දෙන ලෙස ඉල්ලා සිටියේය. ඒ සඳහා ඔබ සැමගේ සහයෝගය ලබා දෙන්නේ නම් ඉදිරියේදී ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ දායකත්වය ලබා දීමට කටයුතු කරන බවත් ඒ සඳහා සභාවේ නිලධාරීන් කටයුතු කරන බවත් සඳහන් කළේය.

ඉන්පසුව සභාපති විසින් ආරාධිත අමුත්තන්ගේ කතා වාරය ඇරඹුණි. ඒ අනුව ජිනදාස මහතා කතා වාරයේදී සභාවේ ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ සහයෝගය ලබා දෙන ලෙස ඉල්ලා සිටියේය. ඒ සඳහා ඔබ සැමගේ සහයෝගය ලබා දෙන්නේ නම් ඉදිරියේදී ගොඩනැඟිලිවල සංවර්ධන කටයුතු සඳහා ඔබ සැමගේ දායකත්වය ලබා දීමට කටයුතු කරන බවත් ඒ සඳහා සභාවේ නිලධාරීන් කටයුතු කරන බවත් සඳහන් කළේය.

යෝජනා හා සහාය දැක්වීමේදී DC 02 සහ DC 03 අදාළ ගණුම් ඒ ඒ සභා වෙත DC 01, DC 02 සහ DC 03 අදාළ ගණුම් ඒ ඒ සභා වෙත ඉදිරිපත් කරන ලදී. ඒ අනුව ඒ ඒ සභා වෙත ඉදිරිපත් කරන ලදී.

කල වේලාව ඉතාමත් ගතවී ඇති බවින් ලේකම් මහතාගේ ස්තුති කතාවෙන් සභාවේ වැඩ කටයුතු අවසන් කරන ලදී. ස්තුතියි.

වෙයට
ලේකම්.

List of Attendence

2026/09/15 දින අමති [illegible] සාමාන්‍ය නාම

ලේඛනය.

	නම.	~~[illegible]~~	[illegible]			අත්සන
1.	[illegible]	5190, [illegible], [illegible]				[illegible]
2	H [illegible]					
3		16.	[illegible]			[illegible]
4	[illegible]	19	"	"		[illegible]
5	L.H [illegible]	62	"	"		[illegible]
6	J.A. [illegible]	65	"	"		[illegible]
7	R.K.K. [illegible]	79.	"	"		[illegible]
8	W. [illegible]	70	"	"		[illegible]
9	W. [illegible]	68.	"	"		[illegible]
10	S. [illegible]	52	"	"		[illegible]
11	R.T [illegible]	11	"	"		[illegible]
12	[illegible]	09	"	"		[illegible]
13	M.A [illegible]	67	"	"		[illegible]
14	[illegible]	40	"	"		[illegible]
15	[illegible]	45	"	"		[illegible]
16	[illegible]	66	"	"		[illegible]
17	B.A. [illegible]	37	"	"		[illegible]
18	[illegible]	46	"	"		[illegible]
19	J.S [illegible]	15.	"			[illegible]
20	K.B.G. [illegible]	17,	"	"		Menaka
21	J.P. [illegible]	72	"	"		[illegible]
22	K.L [illegible]	10	"	"		[illegible]
23	G.L [illegible]	21	"			[illegible]
	S. [illegible]	02	"			[illegible]

24	R. [illegible]	[illegible]	[illegible]
25	J.M. [illegible]	[illegible]	[illegible]
26	USB [illegible]	[illegible]	[illegible]
27	M. [illegible]	නො 2428 [illegible]	[illegible]
28	SW [illegible]	[illegible]	[illegible]
29	I.P [illegible]	[illegible]	Yamaha
30	I.P [illegible]	[illegible]	[illegible]
31	W.G [illegible]	[illegible]	[illegible]
32	P [illegible]	[illegible]	[illegible]
33	[illegible]	[illegible]	[illegible]
34	[illegible]	[illegible]	[illegible]
35	[illegible]	[illegible]	[illegible]
36	K.G [illegible]	[illegible]	[illegible]
37	M.H.S [illegible]	[illegible]	Sadesh
38	M.H [illegible]	[illegible]	[illegible]
39	[illegible]	[illegible]	[illegible]
40	A.G [illegible]	[illegible]	Guyuni
41	[illegible]	H 197/A [illegible]	[illegible]
42	PH [illegible]	[illegible]	[illegible]
43	BU [illegible]	[illegible]	[illegible]
44	R [illegible]		

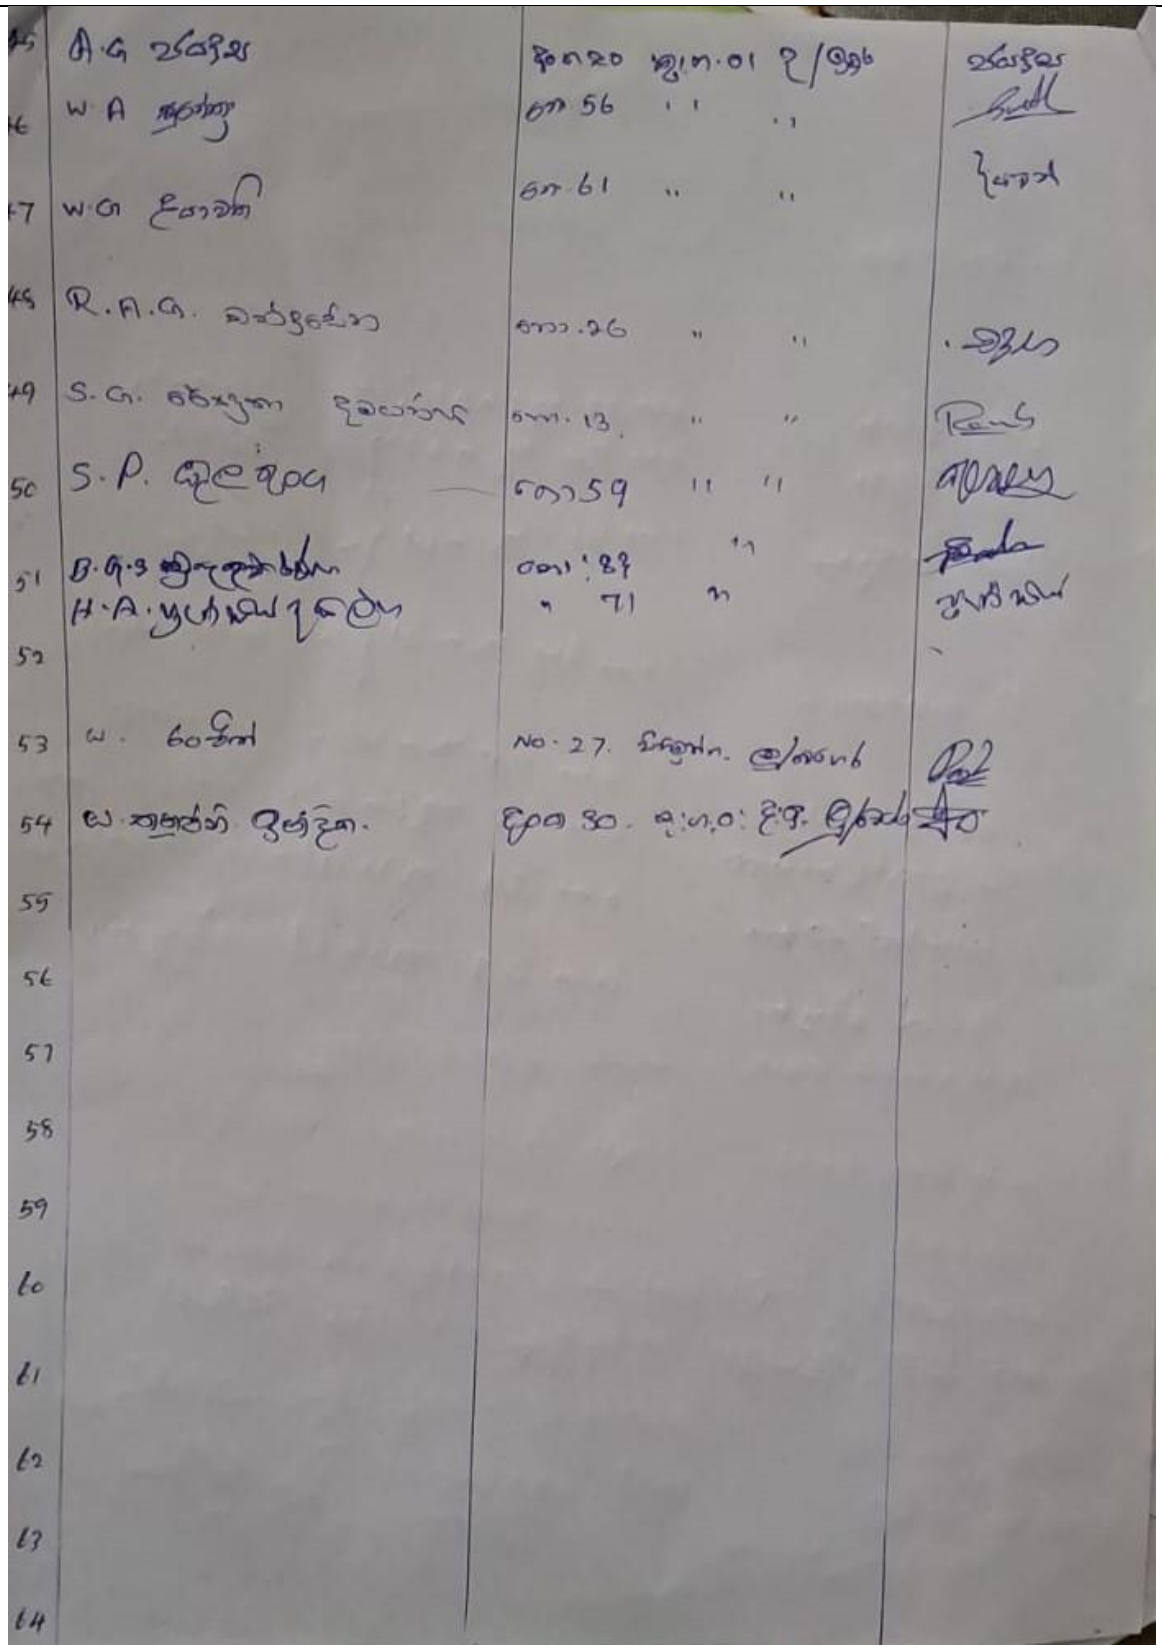

Photographs





Annex 04: Social Management Plan (SMP)

Distribution Canal (DC 1) Improvement Project, Track one of Lunugamvehera Left Bank Main Canal (LBMC)

This Social Management Plan shall be read together with the Environmental Management Plan (EMP) provided with the Environmental Screening Report dated 17th September 2026. It is a mandatory document for signing contractors to ensure social compliance with the World Bank's Environmental and Social Framework (ESF). The contractor is responsible for preparing the Social Management Action Plan (SMAP) based on this Plan, which shall be implemented to avoid or mitigate possible adverse social impacts during the construction period. The individual Worker Code of Conduct in Annex 3 shall also be included in the contract agreement.

No	Potential Environmental / Social Impacts	Mitigation Measures	Implementing Place	Implementing Cost	Responsibility	Time Frame
1	**Institutional Arrangement**					
	Inadequate monitoring or failure to enforce EMP compliance during construction.	• Employ an Environmental, Occupational Health, and Safety (EOHS) Officer through the Project Implementation Agency.	Project / Sub-project Site	Construction Cost	Irrigation Department (ID) / PMU	Entire Construction Phase
		• EOHS Officer shall develop and execute an OHS inspection checklist based on the EMP to monitor contractor compliance.	Do	Do	Do	Do
2	**Legal & EMP Compliance**					
	Non-compliance with statutory regulations and approved environmental safeguards.	• Coordinate with Farmer Organizations (FOs) to avoid construction during peak agricultural activities.	Site	Construction Cost	Irrigation Department	Entire Construction Phase
		• Strictly adhere to mitigation measures in the EMP provided in the Environmental Screening Report (17 Sept 2026).	Do	Do	Do	Do
3	**Water Management & Livelihoods**					
	Unscheduled water cuts, extended shutoffs (>3 days), or land prep	• Schedule major civil works exclusively during the off-season.	DC 1 Canal & Command Area	Contractor's Cost	Irrigation Department / Contractor	Construction Period

	delays disrupting crop planting and yield.	• Provide adequate water for initial land preparation/mudwork.	Do	Do	Do	Do
		• Strictly adhere to the rotational schedule (4 days water supply / 3 days shutoff).	Do	Do	Do	Do
		• Include binding compliance clauses in construction contract documents.	Do	Do	Do	Do
		• Install temporary bypass channels/pipes if canal rehabilitation obstructs flow.	Do	Do	Do	Do
		• Conduct early participatory consultations with FOs and farmers prior to construction.	Do	Do	Do	Do
4	**Access Management & Traffic Safety**					
	Machinery movement, trenching, stockpiling, and overnight hazards obstructing DC 1 service road and risking traffic/farmer safety.	• Maintain uninterrupted traffic access along the DC 1 service road throughout construction.	DC 1 Service Road & Storage Yards	Contractor's Cost	Irrigation Department / Contractor	During Construction
		• Deploy dedicated flaggers/traffic controllers.	Do	Do	Do	Do
		• Post informational signage, speed limit indicators, and advance warning markers.	Do	Do	Do	Do
		• Erect rigid hard barricading around deep cuts, open excavations, and exposed rebar.	Do	Do	Do	Do
		• Restrict material stockpiling to designated, demarcated off-road zones.	Do	Do	Do	Do
		• Mandate daily site cleanup, formwork stripping, and trench covering/backfilling before shift end.	Do	Do	Do	Do
		• Arrange designated parking for construction equipment away from public lanes.	Do	Do	Do	Do

5	**Occupational Health & Safety (OHS)**					
	Safety risks to workers, local farmers, and commuters from heavy machinery, open pits, and site hazards.	• Comply with Factory Ordinance safety standards across site and storage yards.	Site & Material Storage Areas	Contractor's Cost	Irrigation Department / PMU / Contractor	During Construction (Training prior to start)
		• Provide standard PPE (helmets, high-visibility vests, boots) and enforce safe work methods.	Do	Do	Do	Do
		• Conduct basic H&S training for all workers prior to commencement.	Do	Do	Do	Do
		• Maintain basic emergency first-aid facilities on site.	Do	Do	Do	Do
		• Clear and fully reinstate work camps and storage sites after construction completion.	Do	Do	Do	Do
5.1	**Specific OHS: Venomous Snake Hazards**					
	High risk of venomous snake encounters during vegetation clearing and manual canal lining.	• Conduct daily morning toolbox talks on venomous snake identification and bite prevention.	Active Work Sites along DC 1	Contractor's Cost	Irrigation Department / Contractor	During Clearing & Lining Works
		• Provide workers handling brush/masonry with high-ankle safety boots (or snake guards) and heavy gloves.	Do	Do	Do	Do
		• Ensure site supervisors hold valid certification in basic snakebite management (immobilization protocols; no cutting/suctioning).	Do	Do	Do	Do
		• Maintain fully stocked first-aid kits with pressure immobilization bandages.	Do	Do	Do	Do
		• Keep a dedicated emergency transport vehicle on standby during working hours.	Do	Do	Do	Do

6	**Land-Related Impacts**					
	Temporary or permanent land encroachment, private property damage, or unauthorized land use.	• Prohibit trespassing, encroachment, or damage to private property or residential structures near the service road.	Construction Corridor	Contractor's Cost	Irrigation Department	During Construction
		• Confine all construction activities strictly within the designated right-of-way (ROW).	Do	Do	Do	Do
7	**Labor Management, Camps & GBV/SEA/SH**					
	Socio-cultural conflicts, inadequate worker living conditions, wage disparity, child labor, and risks of GBV/SEA/SH.	• Locate labor camps at a safe distance from sensitive community sites.	Camp / Work Yard / Site	Contractor's Cost	Irrigation Department / IRDCRP / Contractor	During Construction
		• Ensure camps meet IFC standards (ventilation, clean water, sanitation: 1 toilet per 15 persons with gender separation).	Do	Do	Do	Do
		• Prioritize hiring local labor and FO members to reduce labor influx.	Do	Do	Do	Do
		• Require all workers to sign an individual Code of Conduct covering ESHS and strictly prohibiting GBV/SEA/SH.	Do	Do	Do	Do
		• Conduct mandatory health/hygiene and GBV prevention awareness sessions.	Do	Do	Do	Do
		• Enforce wage parity and ban child labor (<16 yrs) or hazardous tasks for minors (16–18 yrs).	Do	Do	Do	Do
		• Maintain an updated labor registry (Names, NICs, Addresses) with the PMU/ID.	Do	Do	Do	Do

8	**Solid Waste Management**					
	Accumulation and improper disposal of construction debris and domestic solid waste.	• Implement waste segregation, reuse, and disposal protocols in accordance with the project EMP.	Site & Camps	Contractor's Cost	Irrigation Department / Contractor	During Construction
		• Prohibit indiscriminate dumping along the reservoir reservation or canal banks.	Do	Do	Do	Do
9	**Grievance Redress Mechanism (GRM)**					
	Complaints from cultivators, commuters, or residents regarding construction disruptions.	• Maintain a three-tier GRM including a Site-Level Grievance Redress Committee (GRC) and Social Audit Committee (SAC).	Site Office	Contractor's Cost	Irrigation Department / Contractor	Construction Period
		• Hold monthly GRC meetings with community representatives.	Do	Do	Do	Do
		• Maintain an active Complaints Registry and Complaint Box at the site office.	Do	Do	Do	Do
10	**Contingency Measures & Livelihood Support**					
	Water supply disruptions, project delays, or extreme weather causing crop failure or income loss.	• Implement alternative engineering solutions (cofferdams, bypass canals, staggered construction).	Rehabilitation Area	Contractor's Cost / IRDCRP	Irrigation Department / IRDCRP	During Construction
		• Provide bowsers/pumps if drinking, domestic, or irrigation sources are accidentally disrupted.	Do	Do	Do	Do
		• Offer short-term skill development or special assistance packages (e.g., seeds/plants) to vulnerable households (female-headed, elderly) if impacts occur.	Do	Do	Do	Do
11	**Site Reinstatement**					
	Unrestored stockyards, damaged access roads, unbackfilled pits, or debris left post-construction.	• Full reinstatement of damaged roads, temporary canals, stockyards, and public/private structures required prior to final payment approval.	Construction Area	Contractor's Cost	Irrigation Department / IRDCRP	Project Completion
		• ID and IRDCRP Social/Environmental units to inspect and certify site clearance before final bill release.	Do	Do	Do	Do

12	**Post-Rehabilitation & Recovery**					
	Long-term operational issues or delayed recovery of agricultural productivity.	• Provide post-construction capacity-building training for FOs on sustainable water management.	Rehabilitated DC 1 Command Area	Contractor / IRDCRP	Irrigation Department / IRDCRP	Post-Rehabilitation Phase
		• Monitor agricultural recovery post-rehabilitation and deliver targeted support if recovery is delayed.	Do	Do	Do	Do
13	**SMAP Preparation**					
	General management plans into actionable contractor site workflows.	• Contractor must prepare a Site-Specific Social Management Action Plan (SMAP) aligned with this EMP and obtain approval from the Senior Social Development Specialist (IRDCRP) prior to work commencement.	Construction Area	Contractor's Cost	Irrigation Department / IRDCRP	Prior to Construction

Annex 05: Individual Code of Conduct (with Sinhala Version)

Individual Code of Conduct

Implementing Environmental, Social, Health and Safety (ESHS), Occupational Health and Safety (OHS) Standards, Sexual Exploitation and Abuse (SEA), Sexual Harassment (SH) and Preventing Gender Based Violence (GBV).

I, _____, acknowledge that adhering to Environmental, Social, Health and Safety (ESHS) standards, following the project's Occupational Health and Safety (OHS) requirements, preventing Gender Based Violence (GBV), Sexual Exploitation and Abuse (SEA), Sexual Harassment (SH) is important. The company considers that failure to follow ESHS and OHS standards, or to partake in activities constituting GBV-be it on the work site, the work site surroundings, at workers' camps, or the surrounding communities-constitute acts of gross misconduct and are therefore grounds for sanctions, penalties or potential termination of employment. Prosecution by the Police of those who commit GBV may be pursued if appropriate.

I agree that while working on the project I will:

1. Consent to Police background check.
2. Attend and actively partake in training courses related to ESHS, OHS, SEA, SH and GBV as requested by my employer.
3. Will wear my personal protective equipment (PPE) at all times when at the work site or engaged in project related activities.
4. Take all practical steps to implement the contractor's environmental and social management plan (C-EMP).
5. Implement the OHS Management Plan.
6. Adhere to a zero-alcohol policy during work activities, and refrain from the use of narcotics or other substances which can impair faculties at all times.
7. Treat women, children (persons under the age of 18), and men with respect regardless of race, color, language, religion, political or other opinion, national, ethnic or social origin, property, disability, birth or other status.
8. Not use language or behaviour towards women, children or men that is inappropriate, harassing, abusive, sexually provocative, demeaning or culturally inappropriate.
9. Not sexually exploit or abuse project beneficiaries and members of the surrounding communities.
10. Not engage in sexual harassment of work personnel and staff —for instance, making unwelcome sexual advances, requests for sexual favors, and other verbal or physical conduct of a sexual nature is prohibited. E.g. looking somebody up and down; kissing, howling or smacking sounds; hanging around somebody; whistling and catcalls; in some instances, giving personal gifts.
11. Not engage in sexual favors —for instance, making promises of favorable treatment (e.g. promotion), threats of unfavorable treatment (e.g. loss of job) or payments in kind or in cash, dependent on sexual acts—or other forms of humiliating, degrading or exploitative behaviour.
12. Not use prostitution in any form at any time.
13. Not participate in sexual contact or activity with children under the age of 18—including grooming, or contact through digital media. Mistaken belief regarding the age of a child is not a defence. Consent from the child is also not a defence or excuse.

14. Unless there is the full consent[1] by all parties involved, I will not have sexual interactions with members of the surrounding communities. This includes relationships involving the withholding or promise of actual provision of benefit (monetary or non-monetary) to community members in exchange for sex (including prostitution). Such sexual activity is considered "non-consensual" within the scope of this Code.
15. Consider reporting through the GRM or to my manager any suspected or actual GBV by a fellow worker, whether employed by my company or not, or any breaches of this Code of Conduct.

With regard to children under the age of 18:

16. Bring to the attention of my manager the presence of any children on the construction site or engaged in hazardous activities.
17. Wherever possible, ensure that another adult is present when working in the proximity of children.
18. Not invite unaccompanied children unrelated to my family into my home, unless they are at immediate risk of injury or in physical danger.
19. Not use any computers, mobile phones, video and digital cameras or any other medium to exploit or harass children or to access child pornography (see also "Use of children's images for work related purposes" below).
20. Refrain from physical punishment or discipline of children.
21. Refrain from hiring children for domestic or other labour below the minimum age of 14 unless national law specifies a higher age, or which places them at significant risk of injury.
22. Comply with all relevant local legislation, including labour laws in relation to child labour and World Bank's safeguard policies on child labour and minimum age.

Use of children's images for work related purposes When photographing or filming a child for work related purposes, I must:

23. Before photographing or filming a child, assess and endeavor to comply with local traditions or restrictions for reproducing personal images.
24. Before photographing or filming a child, obtain informed consent from the child and a parent or guardian of the child. As part of this I must explain how the photograph or film will be used.
25. Ensure photographs, films, videos and DVDs present children in a dignified and respectful manner and not in a vulnerable or submissive manner. Children should be adequately clothed and not in poses that could be seen as sexually suggestive.
26. Ensure images are honest representations of the context and the facts.
27. Ensure file labels do not reveal identifying information about a child when sending images electronically.

With regard to Sexual Harassment in the Construction Site:

I ensure to avoid unwelcome sexual advances, requests for sexual favors, and other verbal or physical conduct of a sexual nature. In this regard I am committed to avoid from:

1. Inappropriate jokes or comments.
2. Unwanted touching or physical advances.

[1] **Consent** is defined as the informed choice underlying an individual's free and voluntary intention, acceptance or agreement to do something. No consent can be found when such acceptance or agreement is obtained using threats, force or other forms of coercion, abduction, fraud, deception, or misrepresentation. In accordance with the United Nations Convention on the Rights of the Child, the World Bank considers that consent cannot be given by children under the age of 18, even if national legislation of the country into which the Code of Conduct is introduced has a lower age. Mistaken belief regarding the age of the child and consent from the child is not a defense.

3. Displaying offensive material.
4. Persistent unwelcome invitations or communications.

Simultaneously avoiding of aforesaid matters, I endeavor to apply SH related following prevention strategies in the construction site:

1. Clear anti-harassment policies.
2. Reporting mechanisms.
3. Regular training and awareness programs.
4. Promoting respect and inclusion.
5. Encouraging open communication.
6. Zero tolerance policy.
7. Immediate action on reports.
8. Thorough and impartial investigations.
9. Support for victims
10. Employee Assistance Programs
11. Protecting the privacy of victims.
12. Role in prevention and response.
13. Understanding rights and responsibilities.
14. Supporting colleagues and reporting incidents.
15. Discuss outcomes and lessons learned.
16. Encouraging diversity and inclusion.
17. Regular feedback and surveys.
18. Adapting to new challenges.

With regard to sexual exploitation and abuse, I shall be committed to avoiding in the construction sites:

1. **Sexual exploitation:** Any actual or attempted abuse of a position of vulnerability for sexual purposes, including profiting monetarily, socially, or politically from the sexual exploitation of another (this includes prostitution, trafficking, and exploitation in the workplace or educational institutions).

2. **Sexual abuse:** actual or threatened physical intrusion of a sexual nature, whether by force or under unequal or coercive conditions (this includes rape, sexual assault, and harassment).

In this effort, I shall be committed to complying with and adhering to the Key Mitigation Principles of the following:

I **Survivor-Centered Approach:** Ensuring safety, confidentiality, and respect for victims.
II **Accountability:** holding perpetrators accountable; organizational responsibility.
III **Prevention:** Proactive measures to prevent SEA.

Sanctions:

I understand that if I breach this Individual Code of Conduct, my employer will take disciplinary action which could include:

I Informal warning.
II Formal warning.
III Additional Training.
IV Loss of up to one week's salary.
V Suspension of employment (without payment of salary), for a minimum period of 1 month up to a maximum of 6 months.
VI Termination of employment.
VII Report to the Police if warranted.

I understand that it is my responsibility to ensure that the environmental, social, health and safety (ESHS), occupational health and safety (OHS) Standards, Sexual Exploitation and abuse (SEA), Sexual Harassment (SH) and Preventing Gender Based Violence (GBV) standards are met. That I will make and adhere to the OHS management plan. Simultaneously, I will adhere to implement GRM in the construction site during the construction period. That I will avoid actions or behaviours that could be construed as GBV. Any such actions will be a breach this Individual Code of Conduct. I do hereby acknowledge that I have read the foregoing Individual Code of Conduct, do agree to comply with the standards contained therein and understand my roles and responsibilities to prevent and respond to SEA, SH, ESHS, OHS, GBV issues. I understand that any action inconsistent with this Individual Code of Conduct or failure to act mandated by this Individual Code of Conduct may result in disciplinary action and may affect my ongoing employment.

Signature: _____

Printed Name: _____

Title: _____

Date: _____

තනි පුද්ගල වයර්ධමර් සංග්‍රහය

පාරිසරික, සමාජීය, සෞඛ්‍ය සහ ආරක්ෂාව, වෘත්තීය සෞඛ්‍ය සහ ආරක්ෂාව සම්බන්ධ ප්‍රමිතින්, ලිංගික සූරාකෑම සහ අපයෝජන, ලිංගික හිරිහැර සහ ස්ත්‍රී පුරුෂ සමාජභාවය පදනම් වූ ප්‍රචණ්ඩත්වය වැළැක්වීම

.....වන මම පාරිසරික, සමාජමය ,සෞඛ්‍ය ,සහ ආරක්ෂාව (ESHS) සම්බන්ධ **ප්‍රමිතින්** පිළිපැදීම ව්‍යාපෘතියේ ,වෘත්තීයමය ,සෞඛ්‍ය සහ ආරක්ෂාවට (OHS) අදාළ අවශ්‍යතාවයන් අනුගමනය කිරීම ,සහ ස්ත්‍රීපුරුෂ සමාජභාවය මත පදනම් වූ හිංසන ක්‍රියාවන් (GBV) වැළැක්වීම වැදගත් බව පිළිගනිමි .වැඩබිම ,වැඩබිම අවට ,කම්කරු කඳවුරුවල හෝ අවටප්‍රජාවන්හීදී වේවා ESHS සහ OHS ප්‍රමිතින් අනුගමනය කිරීමට අපොහොසත්වීම හෝ GBV සම්බන්ධ ක්‍රියා කාරකම්වල නිරතවීම දැඩි විෂමාචාර ක්‍රියාවන් බවට සමාගම සළකන හෙයින් ඒ අනුව ඒවා දඬුවම් පැනවීමට ,දණ්ඩනවලට ලක්කිරීමට හෝ ඇතැම්විට සේවය අවසන් කිරීමට වුවද හේතු වේ .GBV ක්‍රියාවන්වල යෙදෙන්නන්ට විරුද්ධව අවශ්‍ය නම් පොලීසිය විසින් නඩු පැවරීමටද කටයුතු කරනු ඇත.

එබැවින් ව්‍යාපෘතියේ සේවයේ නියුක්තව සිටින අතරතුර දී මෙහි සඳහන් ආචාර ධර්ම පිළිපැදීමට මම එකඟ වෙමි.

1. පොලීසිය විසින් සිදුකරනු ලබන පසුබිම් තොරතුරු සෙවීමට කැමැත්ත පළ කිරීම.
2. මාගේ සේවා යෝජකයාගේ ඉල්ලීම පරිදි ESHS, OHS සහ GBV සම්බන්ධ පුහුණු වැඩසටහන්වලට සහභාගි වීම සහ ඒවාට ක්‍රියාශීලීව සම්බන්ධවීම.
3. වැඩබිමේ සිටින විට දී සහ ව්‍යාපෘතියට සම්බන්ධ කටයුතුවල නිමග්නව සිටිනා සෑම අවස්ථාවකදීම මාගේ පුද්ගලික ආරක්ෂක උපකරණ (PPE) පැළඳගෙන සිටීම.
4. කොන්ත්‍රාත්කරුගේ පාරිසරික සහ සමාජ කළමනාකරණ සැළැස්ම ක්‍රියාත්මක කිරීමට අවශ්‍ය සෑම ප්‍රායෝගික පියවරයන්ම ගැනීම.
5. රැකියාශ්‍රිත සෞඛ්‍ය ආරක්ෂණ කළමනාකරණ සැළැස්ම ක්‍රියාත්මක කිරීම.
6. සේවයේ යෙදී සිටින අවස්ථාවන්හිදී මධ්‍යසාර භාවිතයෙන් තොර ප්‍රතිපත්තිය අනුගමනය කිරීමට සහ මොළයේ ක්‍රියාකාරිත්වයන් නිතරම අඩපණ කරන්නා වූ මත්ද්‍රව්‍ය හෝ වෙනත් අන්තරායකාරී ඖෂධ භාවිතයෙන් වැළකී සිටීම.
7. වගර්ය ,ශරීර වර්ණර්ය ,භාෂාව ,ආගම ,දේශපාලන හෝ වෙනත් මතිමතාන්තර ,ජාතික ,ජනවාගර්ක හෝ සමාජ සම්භවය ,දේපල වත්කම් ,ආබාධිත බව ,උපත හෝ වෙනත් තත්ත්වයන් සළකිල්ලට නොගෙන සියළුම කාන්තාවන්ට ,වයස අවුරුදු18 ට අඩු ළමයින්ට ,සහ පුරුෂයින්ට ගෞරවාන්විත ලෙස සැළකීම.
8. කාන්තාවන්ට ,ළමයින්ට සහ පුරුෂයින්ට නොගැළපෙන හිංසාකාරී ,දෝෂාරෝපණ -බැනවැදීම් ,ලිංගික වශයෙන් ප්‍රකෝපකාරී ,පහත් කොට සළකන්නා වූ, සංස්කෘතික වශයෙන් නුසුදුසු ,ඇමතීම්වලින් හෝ හැසිරීම්වලින් වැළකී සිටීම.
9. ව්‍යාපෘති ප්‍රතිලාභීන් සහ අවට ප්‍රජාවන්හි සාමාජිකයින් ලිංගික සූරාකෑම්වලට හෝ අපයෝජනය කිරීමෙන් වැළකී සිටීම.
10. සේවක පිරිස හා කායර් මණ්ඩලයට ලිංගික හිරිහැර නොකිරීම .උදා -අනාරාධිත ලිංගික වයර්ා සඳහා පෙළඹවීම ලිංගික අනුග්‍රහයන් නොපැතීම සහ ලිංගික ස්වභාවයේ වෙනත් වාචික හෝ ශාරීරික ක්‍රියාවන් සපුරා තහනම් වේ .උදා -කෙනෙකු දෙස පාදාන්තයේ සිට කේශාන්තය දක්වා බැලීම් ;සිපගැනීම් ,උස් හඬින් කථා කිරීම හෝ ශබ්ද කිරීම ;නුසුදුසු ලෙස කෙනෙකු ළඟ ගැවසීම ;සුරුවම් බෑම සහ නොමනා ශබ්ද සහ ලිංගික ස්වභාවය හුවා දැක්වෙන අභිනයන් ;සමහර විටෙක පෞද්ගලික ත්‍යාග ලබා දීම.
11. ලිංගික අනුග්‍රහයන් හි නොයෙළීම - උදා -විශේෂ සැළකිලි පිළිබඳ පොරොන්දු දීම) උදා -සේවයේ උසස් කිරීම වැනි ,(අයහපත් ප්‍රතිවිපාක දක්වන තජර්න) සේවයෙන් පහ කිරීම (හෝ මූල්‍යමය හෝ ද්‍රව්‍යමය ගෙවීම් ,වෙනත් ආකාරයේ නින්දිත ,පහත් හැසිරීම් හෝ පළිගැනීම් සහගත හැසිරීම්.

12. කිසිම විටෙක කිසිම ආකාරයක ගණිකා වෘත්තිය භාවිතා නොකිරීම.
13. ඇඳුම් පැළඳුමින් හෝ ඩිජිටල් මාධ්‍ය හරහා සම්බන්ධවීම් ඇතුළුව වයස අවුරුදු18 ට අඩු ළමයින් සමඟ ලිංගික සම්බන්ධතා හෝ ලිංගික ක්‍රියාවල නොයෙදීම .ළමයකුගේ වයස පිළිබඳව වැරදි නිශ්චය නිදහසට කාරණාවක් නොවේ .දරුවාගේ කැමැත්ත මත එවැන්නක් කිරීමද සමාවට හෝ නිදහසට කරුණක් නොවේ.
14. අදාළ සියළුම පාශ්චයන්හි පූර්ණ කැමැත්ත[2] නොමැතිව ,අවට ප්‍රජාවන්හි සාමාජිකයින් සමඟ ලිංගික සබඳතා මා හට පැවැත්විය නොහැකිය .ප්‍රතිලාභ නොගෙවා රඳවා ගැනීම් හෝ සත්‍ය වශයෙන්ම ප්‍රජාවේ සාමාජිකයින්ට වන පොරොන්දු) මූල්‍යමය හෝ මූල්‍යමය නොවන (සත්‍ය ප්‍රතිලාභවල සැපයීම්) මූල්‍යමය හෝ මූල්‍යමය නොවන (රඳවා ගැනීම් හෝ ලබා දෙන බවට පොරොන්දුවීම් ආදියද මෙයට ඇතුළත් වේ.
15. GBV හිංසනයන් සත්‍ය වශයෙන්ම සිදුවීමේදී හෝ එවැන්නක් යැයි සැක කෙරෙන අවස්ථාවලදී මෙන්ම මෙම වයර්ාධමර් පද්ධතිය කිසියම් ලෙසකින් උල්ලංඝනය වන්නා වූ අවස්ථාවලදී එය සිදු කරන පුද්ගලයා මා අයත් සමාගමේ කෙනෙකු වූවත් නොවූවත් දුක්ගැනවිලි කමිටුවට හෝ මාගේ කළමනාකරුට වාතර්ා කිරීමට සැළකිළිමත් වීම.

වයස අවුරුදු 18 ට අඩු ළමයින් සම්බන්ධයෙන්:

16. ඉදිකිරීම් භූමියේ ළමයින් සිටී නම් හෝ අන්තරාදායක ක්‍රියාකාරකම්වල යෙදී සිටී නම් ඒ බව මාගේ කළමනාකරුගේ අවධානයට යොමු කිරීම.
17. ළමයින් ආසන්නයේ වැඩ කරන විටදී වැඩිහිටි පුද්ගලයෙකු ඒ අසල සිටිය යුතු බවට හැකි සෑම විටකම වග බළා ගැනීම.
18. මාගේ ඥාති නොවන කිසිම දරුවෙකු ,හදිසි තත්ත්වයක් මත වහාම ප්‍රතිකාර කිරීමට අවශ්ය විටෙක හෝ ශාරීරික වශයෙන් අනතුරකට ලක්වීමේ අවදානමක සිටින අවස්ථාවක හැර මාගේ නිවසට තනිව කැඳවා ගැනීමෙන් වැළකී සිටීම.
19. ළමයින් ලිංගික සූරාකෑමට හෝ හිරිහැරයකට ලක් කිරීමට හෝ ළමා අසැබි දශර්න නැරඹීමට ඉඩ සළසන කිසිදු පරිසණයක් ,ජංගම දුරකථන ,වීඩියෝ සහ ඩිජිටල් කැමරා හෝ වෙනත් මාධ්‍යයක් භාවිතා නොකිරීම)පහත සඳහන්“ සේවා අවශ්යතාවයන් සම්බන්ධයෙන් ළමා ඡායාරූප භාවිතා කිරීම ”ද බලන්න
20. ළමයින්ට ශාරීරික දඬුවම් කිරීමෙන් හෝ හික්මවීමෙන් වැළකී සිටීම.
21. නීතියෙන් ඉහළ වයස් සීමාවක් නියම කර නොමැති විටෙක අවම වයස් සීමාව අවුරුදු 14 ට අඩු ළමයින් ගෘහාශ්රිත හෝ වෙනත් ශ්රම අවශ්යතා සඳහා කුලියට යොදා නොගැනීම ;කෙසේ වෙතත් අනතුරක් වීමෙ සැළකිය යුතු අවදානම් තත්ත්වයකට පත් වීමට ඉඩ ඇති අවස්ථාවන්හිදී වයස අවුරුදු 14 ට වැඩි වුවද ළමයින් සේවයේ යොදා ගත නොහැක.
22. ළමා ශ්‍රමයට අදාළ කම්කරු නීති ඇතළු සියළුම දේශීය නීති සහ සහ ළමා ශ්රමය සහ අවම වයස පිලිබඳ ලෝක බැංකුවේ ආරක්ෂණ ප්රතිපත්තිවලට අනුකූලවීම.

සේවා අවශ්යතාවයන් සම්බන්ධයෙන් ළමා ඡායාරූප භාවිතා කිරීම

රැකියා හා සම්බන්ධ අරමුණු සඳහා දරුවෙකු ඡායාරූප ගත කිරීමේදී හෝ රූ ගත කිරීමේදී ,මා විසින්

[2] පුද්ගලයෙකුගේ නිදහස් සහ ස්වේච්ඡා මය අභිප්රා ය ,පිළිගැ නීම ,යමක්කිරීමට එකඟවීම මත පදනම් වූ දැ නුවත් තේරීම කැ මැ ත්ත ලෙසට අර්ථ ගැ න්වී ඇත .එවැනි පිළිගැනීමක් හෝ එකඟතා වයක් ,තර්ජනය කිරීමෙන්ල බලෙන් හෝ අන් ආකා ර වල සංයෝ ජනයන්ගෙන්ල බලෙන් පැ හැ රගෙන යා මෙන්ල වංචා වෙන්ල රැවටීමෙන්හෝ වැ රදි ලෙස නිරූපණය කිරීමෙන් ලබා ගන්නා අවස්ථා වන්හිදී කැ මැ ත්ත නො මැ ති බව සො යා ගත හැ ක .චර්යා ධර්ම පද්ධතිය හඳුන්වා දෙනු ලබන රටෙහි ජා තික නීති සම්පා දනයේ අඩු වයසක් දක්වා නිබුණද ලෝ ක බැංකුව එක්සත් ජා තීන්ගේ සංවිධා නයේ ළමා අයිතිවා සිකම් පිළිබඳ සම්මුතිය අනුව යමින් වයස අවුරුදු18 ට අඩු ළමයින් යනු කැ මැ ත්ත ලබා දිය නො හැ කි අය බවට සලකනු ලබයි .ළමයකුගේ වයස පිළිබඳ වැ රදි විශ්වා සය සහ ළමයා ගේ කැ මැ ත්ත නිදහසට හේතුවක් නොවේ .

23. දරුවෙකු ඡායාරූපගත කිරීමට හෝ රූ ගත කිරීමට පෙර හෝ පෞද්ගලික ඡායාරූප ප්‍රතිනිර්මාණ කිරීමේදී දේශීය සම්ප්‍රදායන් හා සීමාකරණයන් අධ්‍යයනය කිරීම හා අනුගමනය කිරීමට ගතහැකි සියළු ප්‍රයත්නයන් දැරීම.
24. දරුවෙකු ඡායාරූපගත කිරීමට හෝ රූගත කිරීමට පෙර ,දරුවාගෙන් හා දෙමාපියන්ගෙන් හෝ භාරකරුවෙකුගෙන් ඒ පිළිබඳව දැනුවත් කර නිසි කැමැත්ත ලබා ගැනීම .මේ සම්බන්ධයෙන් ඡායාරූපය හෝ චිත්‍රපටය භාවිතා කරන්නේ කෙසේද යන්න පිළිබඳ තේරුම් කරදීමට වගබලා ගැනීම.
25. ඡායාරූප ,චිත්‍රපට ,වීඩියෝ සහ ඩීවීඩී තැටි තුළින් ළමයින් නිරූපණය කිරීමේදී ළමයින්ගේ අභිමානය සහ ගෞරවය සුරක්ෂා වන පරිදි එය කිරීමට වග බලා ගැනීම .ඔවුන් අවාසි සහගත බලපෑම්වලට ලක් නොකිරීමට සහ යටහත් නොකිරීමට වග බලා ගැනීම .ළමයින් සුදුසු පරිදි ප්‍රමාණවත් ලෙස ඇඳුම් ඇඳිය යුතු අතර ලිංගික කාරණා ඉස්මතු නොවන ලෙස අදාළ ඉරියව්වලින් පෙනී සිටින ලෙසට වග බලා ගැනීම.
26. ළමා නියෝජනය කිරීමේදී ඒවා සන්දහර්ය සහ සත්යවාදී කරුණු සමඟ සංගතතාවයෙන් යුක්ත බවට තහවුරු කිරීම.
27. විද්‍යුත් තැපැලෙන් ඡායාරූප යවන විට දරුවෙකු පිළිබඳ හඳුනා ගැනීමේ තොරතුරු ගොනු ලේබල මඟින් අනාවරණය නොවන බවට සහතික වීම.

දණ්ඩනයන්

මා මෙම පුද්ගලානුබද්ධ වයර්ාධමර් පද්ධතිය උල්ලංඝනය කළහොත් ,මාගේ සේවා යෝජකයා මට විරුද්ධව විනය ක්‍රියාමාගර් ගන්නා බවත් ඒවාට පහත දැක්වෙන දණ්ඩනයන් ඇතුළත් විය හැකි බවත් දනිමි.

1. අවිධිමත් අනතුරු ඇඟවීම්
2. විධිමත් අනතුරු ඇඟවීම්
3. අතිරේක පුහුණු කිරීමේ
4. සතියක් දක්වා වැටුප් අහිමිවීම්
5. රැකියාව අත්හිටුවීම) වැටුප් නොගෙවා ,(අවම මාස 1 ක කාලයක සිට උපරිම මාස 6 ක කාලයක් දක්වා
6. රැකියාව අවසන් කිරීම
7. අවශ්ය වුවහොත් පොලීසියට වාතර්ා කිරීම

පාරිසරික ,සමාජමය ,සෞඛ්යමය සහ ආරක්ෂාවට අදාළ ප්රමිතින් සපුරාලීම සහතික කිරීමත්, වෘත්තීයට අදාළ සෞඛ්ය සහ ආරක්ෂක කළමනාකරණ සැලසුම පිළිපැදීමත්, එමෙන්ම ස්ත්රී පුරුෂ සමාජභාවය මත පදනම් වූ හිංසනයන් සේ හැඟවෙන ක්රියාකාරකම්වලින් සහ වයර්ාවන්ගෙන් වැළකී සිටීමත් මගේ වගකීම බව මම තේරුම් ගනිමි .එවැනි ඕනෑම ක්රියාවක් මෙම පුද්ගලානුබද්ධ වයර්ාධමර් පද්ධතිය උල්ලංඝනය කිරීමක් බවට මම අවබෝධ කර ගෙන සිටිමි .ඉහතින් දක්වා ඇති පුද්ගලානුබද්ධ වයර්ාධමර් පද්ධතිය මා විසින් කියවා බැලූ බවත් එහි ඇති ප්රමිතීන්වලට අනුකූලවීමටත් මම එකඟවන බවත් ,ESHS, OHS, GBV ගැටළු ඇති වීම වැළැක්වීමට සහ ඒවාට ප්රතිචාර දැක්වීමට අදාළ මාගේ කායර්භාරයන් සහ වගකීම් මා විසින් පිළිගන්නා බවත් මෙයින් ප්රකාශ කර සිටිමි . මෙම පුද්ගලානුබද්ධ වයර්ාධමර් පද්ධතිය හා නොගැළපෙන ක්රියාවක් සිදුකිරීම හෝ මෙම පුද්ගලානුබද්ධ වයර්ාධමර් පද්ධතියෙන් බලගන්වා ඇති පරිදි ක්රියා කිරීමට අපොහොසත් වීම ,විනයානුකූල පියවර ගැනීමට හේතු වන බවත් ඉන් දැනට මා නියුක්තව සිටින රැකියාවට කිසියම් අහිතකර බලපෑමක් සිදු විය හැකි බවත් මම අවබෝධ කරගෙන සිටිමි.

අත්සන: .....

මුද්‍රිත නාමය: .....

තත්ත්වය/තරාතිරම: .....

දිනය: .....

Annex 06: composition of the GRCs.

Site level/GN level GRC

Representatives	Nature of the membership
Grama Niladari of the area	Chairman
Representative from the ID	Secretary
Representative of IRDCRP (if available)	Member
Representative of Construction Contractor (PM/Safeguard Officer)	Member
Representative of ID	Member
Representative of FO	Member
Female Representative of DS	Member
Representative of a local social organization (NGO/CBO) or religious leader	Member
Any other essential body as needed	Member

DS level GRC

Representatives	Nature of the membership
Divisional Secretary	Chairman
Representative from the ID	Secretary
Grama Niladari of the area	Member
Representative of Construction Contractor	Member
In charge of ID	Member
Representative of IRDCRP (if available)	Member
Female Representative of DS	Member
Representative of a local social organization (NGO/CBO) or religious leader	Member
Chairmen of Farming Organization.	Member

PMU level GRC

Representatives	Nature of the membership
Additional Secretary of relevant Ministry	Chairman
Representative from the IRDCRP (project Director)	Secretary
Divisional Secretary of relevant area	Member
Senior Social Development Specialist	Member
Representative of ID	Member
Representative of a local social organization (NGO/CBO) or religious leader	Member
Any other essential body as needed	Member

A Grievance Registry and complaint box will be situated at the site office, and a representative of IRDCRP/representative of ID employed on-site will oversee the resolution of potential social issues with the PMU-safeguard team. The Senior Social Development Specialist at PMU will monitor the GRM process in a timely and effective manner. The contractor shall have to adhere to this GRM to mitigate possible social issues due to implementing civil work of the construction.

The SDS of IRDCRP will be responsible for the timely training of the committee members in order to enhance capacity building for the smooth functioning of GRC under the capacity building plan.

Annex 07: Legal Framework and World Bank's ESF Policy and Standards

Within the effect zone, the project does not entail any property acquisition, relocation, or land use changes. Beneficiary farmers' livelihoods can, nevertheless, experience minor effects or disruptions. The project will adhere to the following national laws, regulations, and policies in the event that land purchase, relocation, or impacts are required, and any adverse impacts or discrepancies with the World Bank's Environmental and Social Framework (ESF) will be fixed in line with World Bank guidelines:

National Laws, Regulations, and Policies to prevent adverse impacts

- Land Acquisition Act, 1950
- Land Acquisition Regulations, 2008
- Land Acquisition (payment of compensation) Regulations of 2013
- State Lands (recovery of possession) Act No. 7 of 1979
- Temple and Devalagam (compensation) Ordinance, No. 28 of 1944
- National Involuntary Resettlement Policy, 2001
- National Environmental Act (NEA) No. 47/1980
- Factories Ordinance No. 45 of 1942 (occupational safety & health for factories/construction elements)
- Antiquities Ordinance (No. 9 of 1940)
- Public Health legislation (Public Health Ordinance; Health Services Act); Quarantine & Prevention of Diseases Ordinance; emergency / disaster management regulations.
- Agrarian Development Act No. 46 of 2000 (Section 32)

World Bank's Environmental and Social Standards

The World Bank's Environmental and Social Standards (ESS), part of its Environmental and Social Framework (ESF), set requirements for managing environmental and social risks in projects. For this project, the following plans have been developed to comply with the requirements of ESF:

- Environmental and Social Guideline (ESG)
- Environmental and Social Commitment Plan (ESCP)
- Labor Management Plan (LMP)
- Indigenous Peoples Plan (IPP)
- Stakeholder Engagement Plan (SEP)

Therefore, all Social Safeguards Reports (SSR) and Social Management Plans (SMP) is prepared complying with the requirements details in the above instruments.

Annex 08: Contingency plan

Contingency Plan for Recovery of Possible Livelihood Losses of Farmers During Rehabilitation of Projects

1. Introduction:

The construction and rehabilitation of aforesaid agricultural tanks can temporarily affect the livelihoods of farmers who depend on these resources for cultivation and daily income. This contingency plan outlines strategies and measures to minimize, mitigate, and recover potential livelihood losses experienced by farmers during the construction phase. The plan focuses on protecting vulnerable groups, ensuring timely livelihood restoration, and maintaining food security within the affected community.

2. Objectives of the Plan:

- To ensure that the farmers' livelihoods are not permanently disrupted due to construction activities.
- To provide short-term and long-term livelihood support mechanisms for affected farmers
- To promote community participation in decision-making and implementation of mitigation measures.

3. Potential Livelihood Impacts:

Type of Impact	Description	Affected Group
Loss of cropping season	Construction work may block irrigation water supply, delaying or halting cultivation.	Paddy and vegetable farmers
Temporary loss of access to agricultural land	Machinery, materials, or construction boundaries may restrict access to farmlands.	Landowners and tenant farmers
Reduced income from agriculture	Lack of water and access may reduce harvests, leading to income loss.	Farming households
Employment disruption	Local laborers dependent on agricultural work may lose daily wages.	Agricultural laborers
Disturbance to livestock activities	Movement of cattle or buffalo may be restricted due to site fencing or machinery.	Livestock owners

4. Contingency Measures:

4.1. Pre-Construction Phase:	**Initial Screening Process:** Conduct an Environmental and Social Screening considering socio-economic assessment to identify affected farmers, land tenure status, cropping patterns, and income sources. Making SMP, EMP, EMP in resulting screening process. **Community Consultation:** Engage with Farmers' Organizations (FOs), Grama Niladhari (GN), Irrigation Department (ID) to plan construction timing to avoid cultivation periods.

	Awareness Programs: Inform all stakeholders about construction schedules, access routes, alternative arrangements, the Grievance Redress Mechanism (GRM), and the Stakeholder Advisory Committee (SAC) for irrigation and farming.
4.2. Construction Phase:	**Alternative Irrigation Arrangements:** • Provide temporary water channels, pumps, or pipes to ensure water supply for ongoing cultivation. • Schedule construction during the off-season (Yala or Maha) to minimize cropping losses. • Alternative technical options and site-specific, section-by-section construction scheduling should be adopted to minimize disturbances to farming activities. **Income Support Measures:** • Provide temporary employment opportunities in construction activities (e.g., unskilled labor, transport, cleaning). • Introduce food-for-work programs for affected households. **Livestock Support:** • Provide alternative grazing areas and temporary shelter for livestock. • Arrange safe passage routes for livestock movement around construction zones
4.3. Post-Construction Phase	**Rehabilitation of Agricultural Lands (reinstate):** • Ensure the rehabilitation of DC 1 of track 1, LBMC of Lunugamwehera scheme, before the start of the next cultivation season. • Provide community labor or machinery support for land leveling and field preparation. **Livelihood Recovery Programs:** • Conduct capacity-building and training programs on improved water management, organic farming, and crop diversification. • Promote home gardening, small livestock rearing, or value addition enterprises (e.g., rice milling, dairy products) as supplementary income sources. **Monitoring and Evaluation:** • Establish a joint monitoring committee (FO, GN, ID, and project staff) to review livelihood recovery progress. • Conduct periodic follow-up surveys to ensure income restoration and project sustainability.

5. **Institutional Arrangement:**

Institution	Role and Responsibility
IRDCRP / Project Implementing Agency	Lead implementation of mitigation and recovery activities; coordinate with relevant government departments.
Department of Irrigation (ID)	Technical advice, farmer registration, and compensation verification.
Grama Niladhari & Farmers' Organization (FO)	Community mobilization, grievance reporting, and local monitoring.
Social & Environmental Safeguard Team	Ensure ESS-2 and ESS-5 and ESS-10 compliance, maintain grievance mechanism, and monitor implementation effectiveness.

6. Grievance Redress Mechanism (GRM)

A dedicated Grievance Redress Committee (GRC) will address complaints related to livelihood losses. The mechanism ensures that:

- Grievances are recorded, verified, and resolved within a reasonable time frame.
- Farmers can raise concerns without fear of retaliation.
- All cases and resolutions are documented and reported to the Project Management Unit (PMU).

7. Budgetary Provisions:

The Provisional Sum (PS) of the bidding document shall include a budgetary allocation for implementing this contingency plan. Furthermore, the contingency plan shall be directly linked with the EMP/SMP to cover livelihood recovery activities, including:

- Training and capacity building of farmers.
- Monitoring and grievance handling costs.
- Alternative site-specific water provisions (Farming activity), (refer the SMP/EMP)

These budgetary provisions shall discourage compensation (cash payments) for any affected persons. Payment will be made to the contractor based on the measured quantities, and the payment methods are subject to the approval of the responsible engineer in accordance with the safeguard requirements.

8. Summarizing:

This contingency plan ensures that the construction of the project does not result in long-term livelihood losses for farmers. Through proactive planning, transparent alternative actions, and continuous community engagement, affected farmers will be supported to recover their livelihoods sustainably while contributing to the successful implementation of the project.

Annex 09: The consent letter of the farming organization, and beneficiaries name list

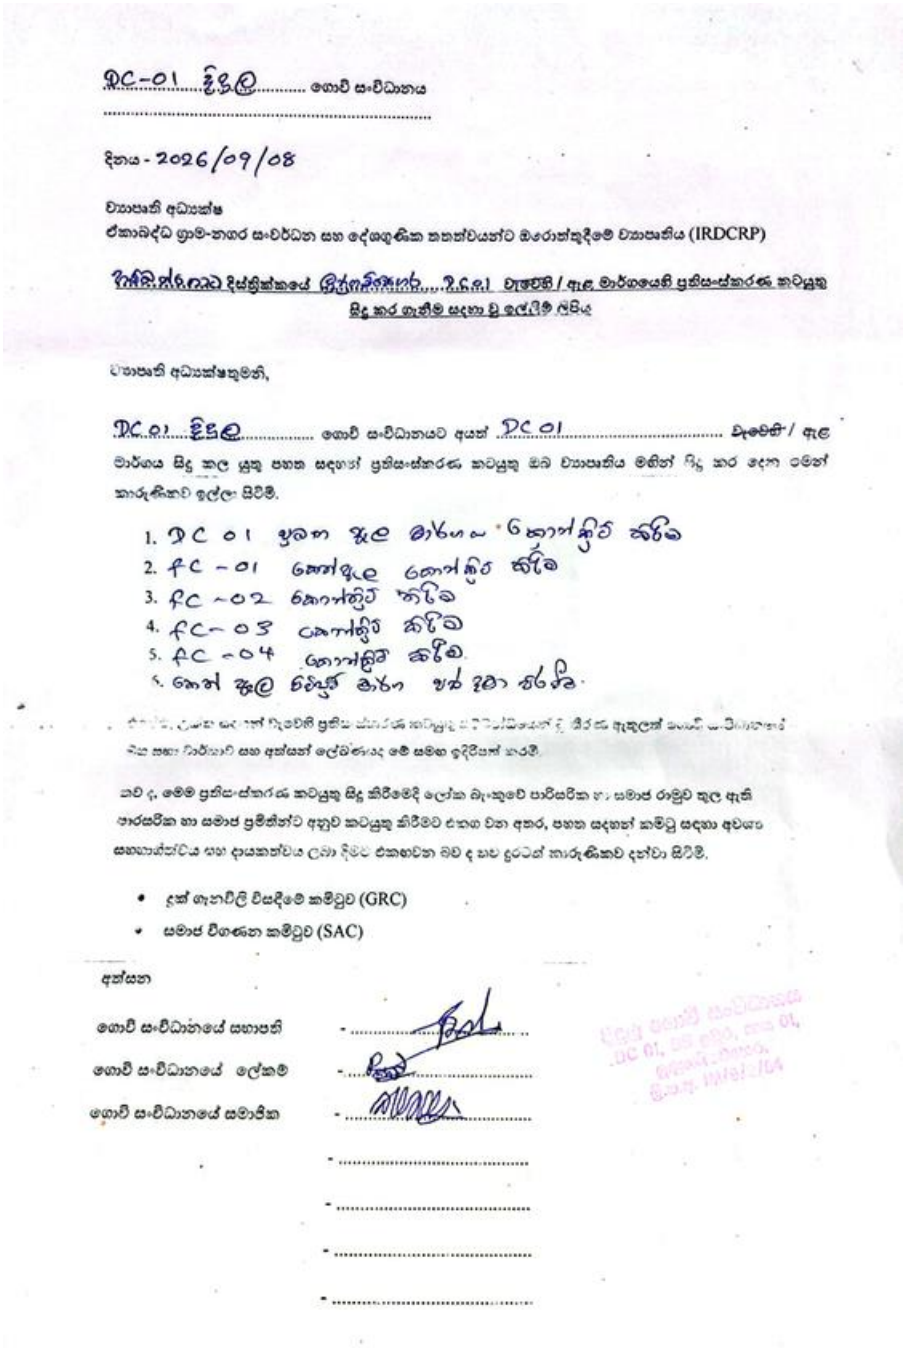

DC-01 දිදුලු ගොවි සංවිධානය

දිනය - 2026/09/08

ව්‍යාපෘති අධ්‍යක්ෂ
ඒකාබද්ධ ග්‍රාම-නගර සංවර්ධන සහ දේශගුණික තත්ත්වයන්ට ඔරොත්තුදීමේ ව්‍යාපෘතිය (IRDCRP)

මහනුවර දිස්ත්‍රික්කයේ මුරුතලාවෙහි DC 01 වැවෙහි / ඇළ මාර්ගයෙහි ප්‍රතිසංස්කරණ කටයුතු සිදු කර ගැනීම සඳහා වූ ඉල්ලීම් පිළිය

ව්‍යාපෘති අධ්‍යක්ෂතුමනි,

DC 01 දිදුලු ගොවි සංවිධානයට අයත් DC 01 වැවෙහි / ඇළ මාර්ගය සිදු කල යුතු පහත සඳහන් ප්‍රතිසංස්කරණ කටයුතු ඔබ ව්‍යාපෘතිය මඟින් සිදු කර දෙන මෙන් කාරුණිකව ඉල්ලා සිටිමි.

1. DC 01 මුලන ඇළ මාර්ගය කොන්ක්‍රීට් කිරීම
2. FC - 01 මෝඇළ කොන්ක්‍රීට් කිරීම
3. FC - 02 කොන්ක්‍රීට් කිරීම
4. FC - 03 කොන්ක්‍රීට් කිරීම
5. FC - 04 කොන්ක්‍රීට් කිරීම
6. කෙත් ඇළ විවුත් කාර්ය වත් දුමා තිරශීම

[illegible] එම සඳහා විවෘතාව සහ අත්සන් ලේඛණයද මේ සමඟ ඉදිරිපත් කරමි.

තව ද, මෙම ප්‍රතිසංස්කරණ කටයුතු සිදු කිරීමෙදී ලෝක බැංකුවේ පාරිසරික හා සමාජ රාමුව තුල ඇති පාරිසරික හා සමාජ ප්‍රමිතීන්ට අනුව කටයුතු කිරීමට එකඟ වන අතර, පහත සඳහන් කමිටු සඳහා අවශ්‍ය සහභාගිත්වය සහ දායකත්වය ලබා දීමට එකඟවන බව ද බහු දුරටත් කාරුණිකව දන්වා සිටිමි.

- දුක් ගැනවිලි විසඳීමේ කමිටුව (GRC)
- සමාජ විගණන කමිටුව (SAC)

අත්සන

ගොවි සංවිධානයේ සභාපති - .....

ගොවි සංවිධානයේ ලේකම් - .....

ගොවි සංවිධානයේ සමාජික - .....

- .....
- .....
- .....
- .....

ඒකාබද්ධ ග්‍රාමනගර සංවර්ධන හා දේශගුණ තත්වයන්ට මරොත්තු දීමේ ව්‍යාපෘතිය - (IRDCRP) - SSR/EN

අත්සන් ලේඛණය 2026.09.

උප ව්‍යාපෘතියේ නම (වැව) - [illegible] වැව 01

දිස්ත්‍රික්කය - [illegible]

ප්‍රා.ලේ. කො. (DS) - [illegible]

ග්‍රා.නි. වසම (GN)- [illegible]

ගොවි සංවිධානය (F/O) - DC -01 [illegible]

අංකය	නම	ආයතනය/ ගොවි සංවිධානයේ නම	තනතුර	ස්ත්‍රී	පුරුෂ	දුරකතන අංකය	අත්සන
1	[illegible]	[illegible]	[illegible]		✓	0773915436	[illegible]
2	R. [illegible]	"			-	0712410119	[illegible]
3	S. [illegible]	"			✓	0703856618.	[illegible]
4	R. [illegible]	"			✓	071-2142317	[illegible]
5	W.S [illegible]	"			✓	0710903969	[illegible]
6	P.M. [illegible]	"				0713177383	[illegible]
7	L.H. [illegible]	"				0718461297	[illegible]
8	R. [illegible]	"			✓	070-4006000	[illegible]
9	[illegible]	"				0756469250	[illegible]
10	[illegible]	"				0718819477	[illegible]
11	S.P [illegible]	"	[illegible]		✓		[illegible]
12	W. [illegible]	"	[illegible]		✓	0774640803	[illegible]

Annex 10: The List of Beneficiaries

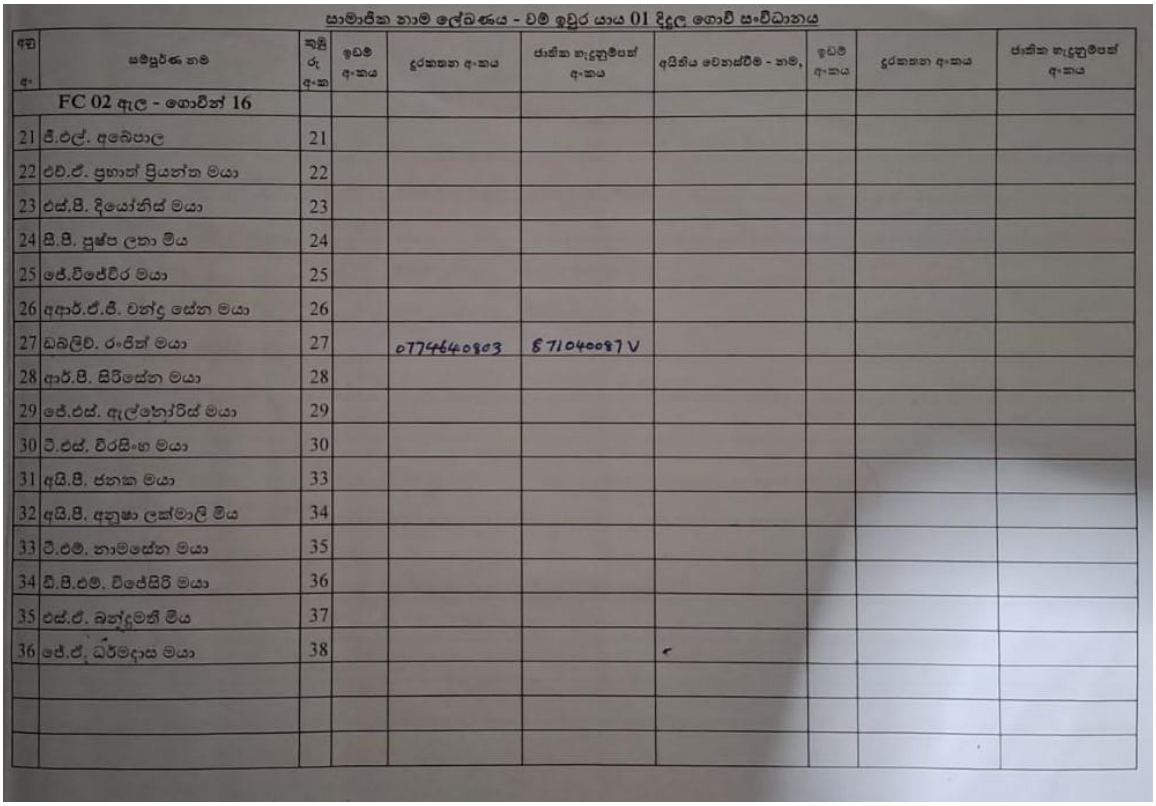

සාමාජික නාම ලේඛණය - වම් ඉවුර යාය 01 දිදුල ගොවි සංවිධානය

අං	සම්පූර්ණ නම	තුලි රු අංක	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය	අයිතිය වෙනස්වීම් - නම,	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය
	FC 02 ඇල - ගොවීන් 16								
21	ජී.එල්. අබේපාල	21							
22	එච්.ඒ. ප්‍රභාත් ප්‍රියන්ත මයා	22							
23	එස්.පී. දියෝනිස් මයා	23							
24	පී.පී. පුෂ්ප ලතා මිය	24							
25	ජේ.විමේචිර මයා	25							
26	අආර්.ඒ.ජී. චන්දු සේන මයා	26							
27	ඩබ්ලිව්. රංජිත් මයා	27		0774640803	871040087V				
28	ආර්.පී. සිරිසේන මයා	28							
29	ජේ.එස්. ඇල්ෆොන්සිස් මයා	29							
30	ටී.එස්. විරසිංහ මයා	30							
31	අයි.පී. ජනක මයා	33							
32	අයි.පී. අනුෂා ලක්මාලි මිය	34							
33	ටී.එම්. නාමසේන මයා	35							
34	ඩී.පී.එම්. විජේසිරි මයා	36							
35	එස්.ඒ. බන්දුමති මිය	37							
36	ජේ.ඒ. ධර්මදාස මයා	38							

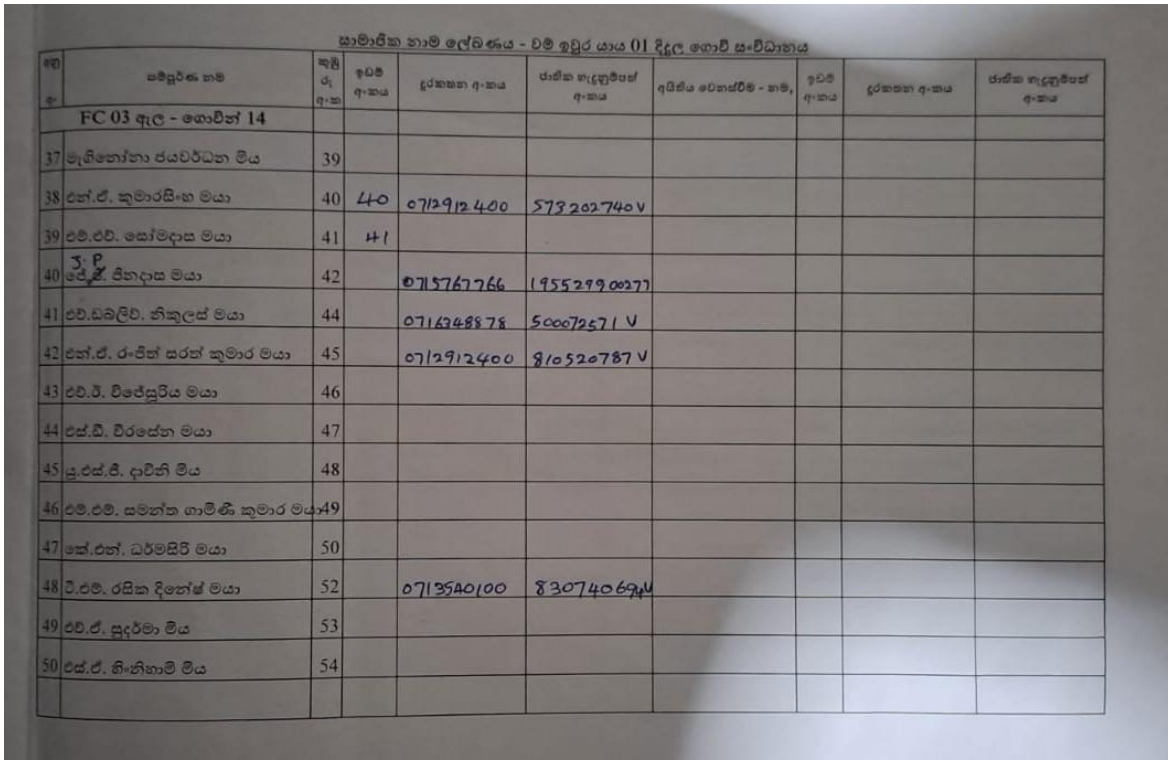

සාමාජික නාම ලේඛණය - වම් ඉවුර යාය 01 දිදුල ගොවි සංවිධානය

අං	සම්පූර්ණ නම	තුලි රු අංක	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය	අයිතිය වෙනස්වීම් - නම,	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය
	FC 03 ඇල - ගොවීන් 14								
37	මැණිනෝනා ජයවර්ධන මිය	39							
38	එන්.ඒ. කුමාරසිංහ මයා	40	40	0712912400	573202740V				
39	එම්.එච්. සෝමදාස මයා	41	41						
40	ජේ.ඒ. ජිනදාස මයා	42		0715767766	195529900277				
41	එච්.ඩබ්ලිව්. නිකුලස් මයා	44		0716348878	500072571V				
42	එන්.ඒ. රංජිත් සරත් කුමාර මයා	45		0712912400	810520787V				
43	එච්.ඩී. විජේසුරිය මයා	46							
44	එස්.ඩී. විරසේන මයා	47							
45	යූ.එස්.ජී. දාවිනි මිය	48							
46	එම්.එම්. සමන්ත ගාමිණී කුමාර මයා	49							
47	කේ.එන්. ධර්මසිරි මයා	50							
48	ටී.එම්. රසික දිනේෂ් මයා	52		0713540100	830740694V				
49	එච්.ඒ. සුදර්මා මිය	53							
50	එස්.ඒ. හිංනිහාමි මිය	54							

සාමාජික නාම ලේඛණය - වම ඉවුර යාය 01 දිදුල ගොවි සංවිධානය

අං	සම්පූර්ණ නම	කුලී රු. අංක	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය	අයිතිය වෙනස්වීම - නම,	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය
	FC 04 ඇල - ගොවීන් 18								
51	ඩබලිව්. ප්‍රියංගනී මිය	55							
52	අජිත් රණවීර මයා	56	56	071 9445362	19797390	W.A සුගන්ති ජටාපුර			
53	එම්.එල්. කරුණාරත්න මයා	57	57	071 3196317	443330623V				
54	ජී.ජී. සුමනසිරි මයා	58							
55	එස්.පී. කුලතුංග මයා	59							
56	කේ.එල්. ඇඩවින් මයා	60							
57	ඩබලිව්.ජී. දයාවති මිය	61		0703983199					
58	එල්.එච්. ධර්මසේන මයා	62							
59	ආර්. කරුණාවති මිය	63							
60	එස්.ඒ. පද්මිනී මිය	64		0714354185	656890185V		64		656390185V
61	ජේ.ඒ. සිරිසේන මයා	65		0710532065	542812648V				
62	එච්.ඒ. සිරියාවති මිය	66		0712912400	196076301846				
63	එම්.ඒ. විජිත මයා	67		0711253600				0717948906	750571778V
64	ඒ.පී.ශෂිකලා හංසමාලි මිය	68		0775735990	998663660 V				
65	ජී.එච්.ගාමිණී මයා	69		0714354185V			64		
66	විදුර අංජන විජේතුංග මයා	70		0775735990	940190142 V				
67	එච්.ඒ. ප්‍රැන්සිස්ද සිල්වා මයා	71		0701152079	680011141V				
68	M.M ඒ.ඒම්. ශ්‍රියානි මිය	72		0715660813	196475400600				

සාමාජික නාම ලේඛණය - වම ඉවුර යාය 01 දිදුල ගොවි සංවිධානය

අං	සම්පූර්ණ නම	කුලී රු. අංක	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය	අයිතිය වෙනස්වීම - නම,	ඉඩම් අංකය	දුරකතන අංකය	ජාතික හැඳුනුම්පත් අංකය
	FC 05 ඇල - ගොවීන් 09								
69	ඩබලිව්.පී. ලීලාවති මිය	73							
70	P.M ටී.එම්. විමලසේන මයා	74		071-3177393	195502802542				
71	බී.එච්. දුෂාන් මයා	75							
72	බී.ජී. සොමිපාල මුතුකුමාරණ මයා	76		0773915736	194929010020				
73	බී.යූ. කපිල මයා	77		0712819477	680153370V				
74	ඩබලිව්.ඒ.කේ. විරසිංහ මයා	78							
75	ඉංදික මයා	79							
76	එල්.ඒ. මල්ලිකා මිය	80							
77	ඩබලිව්.එම්. පියදාස මයා	81			530411095V				

.Annex 11: Asset clearance letter of ID

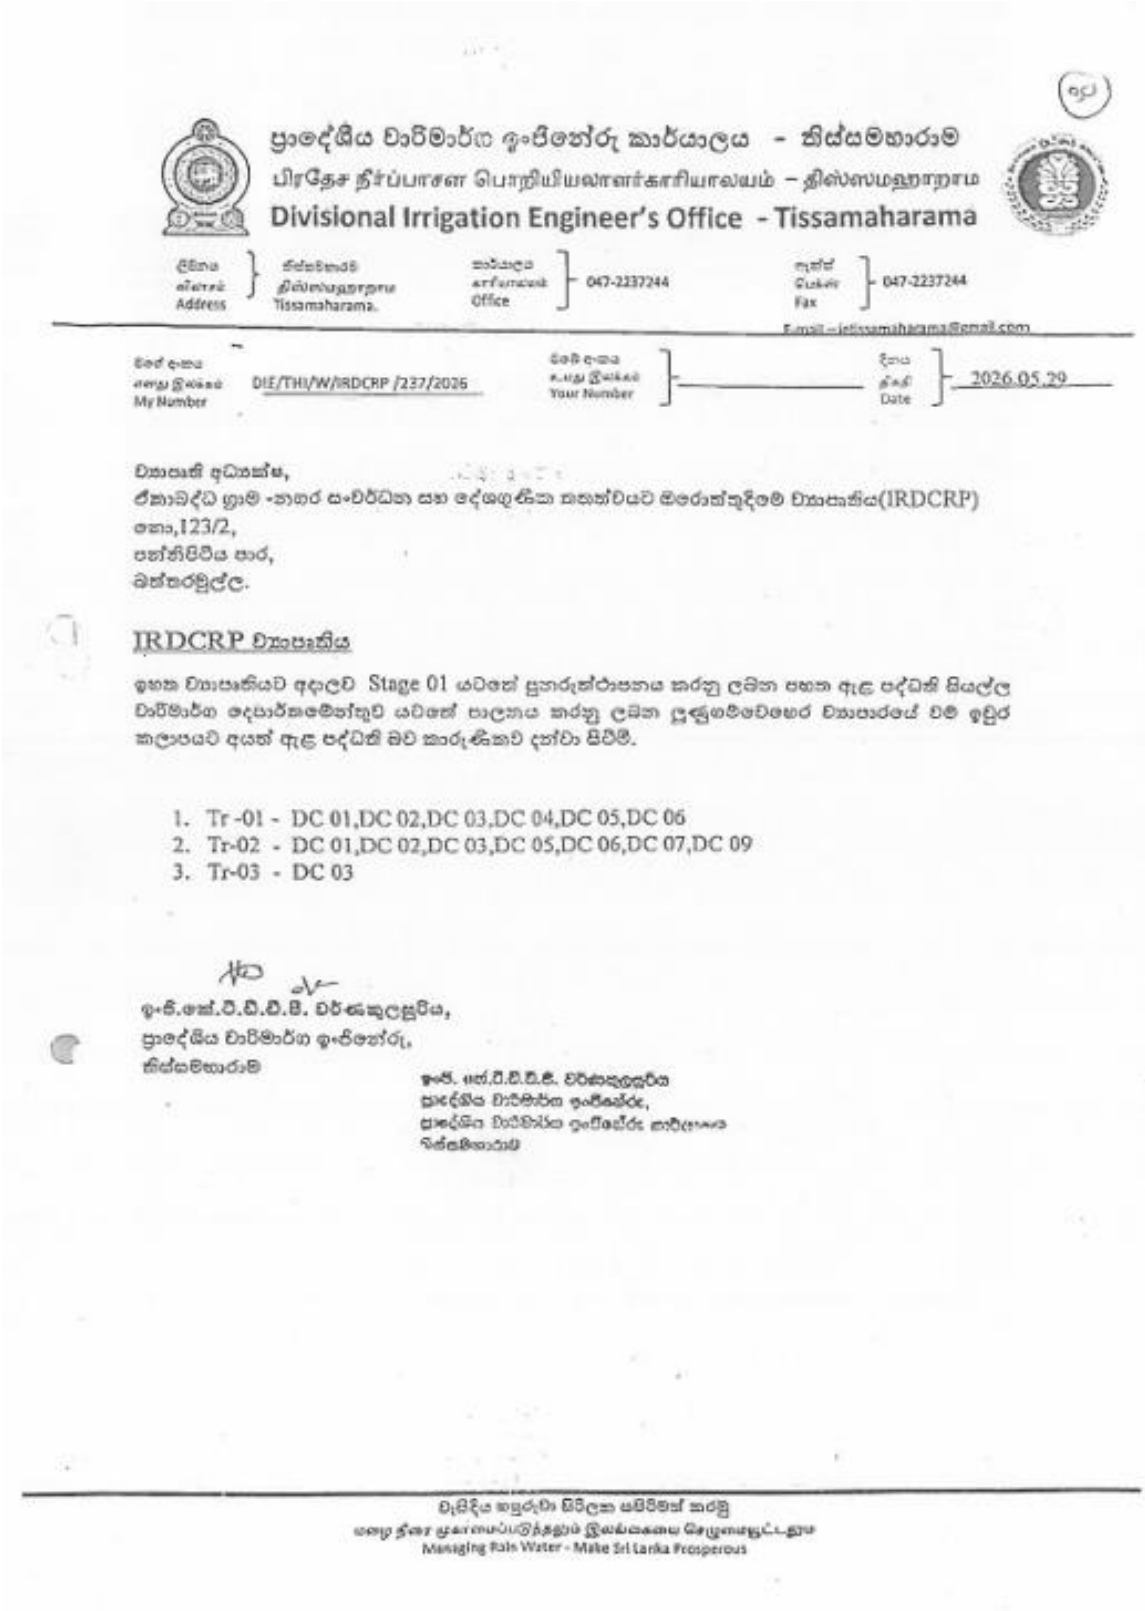

ප්‍රාදේශීය වාරිමාර්ග ඉංජිනේරු කාර්යාලය - තිස්සමහාරාම
பிரதேச நீர்ப்பாசன பொறியியலாளர்காரியாலயம் – திஸ்ஸமஹாராம
Divisional Irrigation Engineer's Office - Tissamaharama

ලිපිනය / விலாசம் / Address: තිස්සමහාරාම திஸ்ஸமஹாராம Tissamaharama.
කාර්යාල / காரியாலய / Office: 047-2237244
ෆැක්ස් / பெக்ஸ் / Fax: 047-2237244
E-mail – pdtissamaharama@gmail.com

මගේ අංකය / எமது இலக்கம் / My Number: DIE/THI/W/IRDCRP /237/2026
ඔබේ අංකය / உமது இலக்கம் / Your Number: -
දිනය / திகதி / Date: 2026.05.29

විධායක අධ්‍යක්ෂ,
ජීකාබද්ධ ග්‍රාම -නගර සංවර්ධන සහ දේශගුණික තතන්වයට ඔරොත්තුදීමේ ව්‍යාපෘතිය(IRDCRP)
අංක,123/2,
පන්නිපිටිය පාර,
බත්තරමුල්ල.

IRDCRP ව්‍යාපෘතිය

ඉහත ව්‍යාපෘතියට අදාලව Stage 01 යටතේ පුනරුත්ථාපනය කරනු ලබන පහත ඇළ පද්ධති සියල්ල වාරිමාර්ග දෙපාර්තමේන්තුව යටතේ පාලනය කරනු ලබන පුළුගහවෙහෙර ව්‍යාපාරයේ වම ඉවුර කලාපයට අයත් ඇළ පද්ධති බව කාරුණිකව දන්වා සිටිමි.

1. Tr -01 - DC 01,DC 02,DC 03,DC 04,DC 05,DC 06
2. Tr-02 - DC 01,DC 02,DC 03,DC 05,DC 06,DC 07,DC 09
3. Tr-03 - DC 03

ඉංජි.කේ.ටී.ඩී.ඒ.ඒ. වර්ණකුලසූරිය,
ප්‍රාදේශීය වාරිමාර්ග ඉංජිනේරු,
තිස්සමහාරාම

ඉංජි. කේ.ටී.ඩී.ඒ.ඒ. වර්ණකුලසූරිය
ප්‍රාදේශීය වාරිමාර්ග ඉංජිනේරු,
ප්‍රාදේශීය වාරිමාර්ග ඉංජිනේරු කාර්යාලය
තිස්සමහාරාම

වැසිදිය කළමනාකරණය කිරීමෙන් සමෘද්ධිමත් ශ්‍රී ලංකාවක්
மழை நீரை முகாமைப்படுத்தலும் இலங்கையை செழுமையுட்டலும்
Managing Rain Water - Make Sri Lanka Prosperous

.Annex 12: BOQs

ESTIMATE OF THE EXPENCE NECESSARY TO BE INCURRED FOR REHABILITATION OF DC 01 FROM 0+150 TO 0+810 TRACT 01 LBMC LUNUGAMWEHERA SCHEME IN TISSAMAHARAMA DIVISION - IRDCRP 2026

SUMMARY OF ESTIMATE

PACKAGE NO :-

Bill No	Description	Amount (LKR)
Bill No 01	Preliminaries(4% of Basic Cost)	475,869.47
Bill No 02	Rehabilitation of DC 01 from 0+150 TO 0+810 Tract 01 LBMC	13,800,214.61
A	Sub Total - Summary of Bills 1 & 2	14,276,084.08
B	Physical Contingencies (Approximately 10% x A)	1,426,731.30
C	Price Contingencies (3% xA)	428,282.52
D	Compliance with Environmental and Social code of Practice (ESCOP)- Provisional Sum (2.5% xA)	356,902.10
E	Sub Total (B+C+D)	2,211,915.92
F	TOTAL ESTIMATED COST (A+E)	16,488,000.00
	VAT – 18% of (F)	2,967,840.00
	Grand Total including VAT	**19,455,840.00**

Bill No 02 **REHABILITATION OF DC 01 FROM 0+150 TO 0+810 TRACT 01 LBMC**

OH & PF (without Preliminaries) E * = 16%

Preliminaries P = 4%

SI No	Description	Unit	Qty (A)	Rate (D=B*(1+E))	Amount F=A*D
2.1	Secondary Growth Jungle clearing and removing debries out side the reservation as directed by machinery.	ha	0.64	46,150.00	29,536.00
2.2	Earth excavation and spoil to waste Cut 0-1.5m lift upto 1.5m spread 30m as directed by machinery.	m^3	100.32	365.50	36,666.96
2.3	Supplying, fixing & removing for 600 x 450 x 150mm size polysag sand baging for coffer damming as directed by manually.	Nos	7.00	438.50	3,069.50
2.4	Dealing with water during construction period using 50 mm dia water pump with fuel and operator	Hrs	75.00	642.50	48,187.50
2.5	Supplying & laying polythene 36/500 Gauge (150 g/m^2)	m^2	363.00	188.50	68,425.50
2.6	Mixing, Placing, compaction of Grade 15 Screed concrete (1:3:6) (Grade metal mix 5mm-25mm) including local transports. Lift up to 1.5 m haul 30 m by machinery.	m^3	18.15	36,125.00	655,668.75
2.7	Furnishing, transporting, cutting tor steel reinforcement bars (RB500) in to required sizes, bending and binding with binding wires including local transport	Kg	5052.79	526.00	2,657,767.54
2.8	Supplying making & fixing 18 mm thick Ordinary Plywood formworks for each of 6 uses & removing same once including loading and unloading.	m^2	847.00	3,791.00	3,210,977.00

2.9	Mixing, Placing, compaction of Grade 20 concrete (1:2:4) (Grade metal mix 5mm-20mm) using poker vibrator. Slump shall be less than 150mm and curing shall be done for 28 days. Form work measured separately, including local transports.Lift up to 1.5 m haul 30 m by machinery.	m^3	112.53	40,553.00	4,563,429.09
2.10	Providing construction joint using 25 mm thick regiform sheets at 11.6m intervels as directed.	m^2	9.30	811.00	7,542.30
2.11	Supplying, Tranporting, Placing & copm. Earth in canal using 3T vibrating roller including watering. Cut 0 - 1.5m, lift upto 1.5m, haul 15000m by tractor trailor.	m^3	620.27	3,461.00	2,146,754.47
2.12	Making boundary stones for D Canal reservation path.	Nos	34.00	6,535.00	222,190.00
2.13	Furnish & install Name boards	Item	Allow	P.Sum	50,000.00
2.14	Fixing & Installing of Gauge & Current meatering the canals & draw the discharge graphs.	Item	Allow	P.Sum	100,000.00
Bill No 02 Sub Total Cost					13,800,214.61

ESTIMATE OF THE EXPENCE NECESSARY TO BE INCURRED FOR REHABILITATION OF DC 01 FROM 0+810 TO 1+189 TRACT 01 LBMC LUNUGAMWEHERA SCHEME IN TISSAMAHARAMA DIVISION - IRDCRP 2026

SUMMARY OF ESTIMATE

PACKAGE NO :-

Bill No	Description	Amount (LKR)
Bill No 01	Preliminaries(4% of Basic Cost)	687,676.68
Bill No 02	Rehabilitation of DC 01 from 0+810 TO 1+189 Tract 01 LBMC	19,942,623.78
A	Sub Total - Summary of Bills 1 & 2	20,630,300.46
B	Physical Contingencies (Approximately 10% x A)	2,062,033.01
C	Price Contingencies (3% xA)	618,909.01
D	Compliance with Environmental and Social code of Practice (ESCOP)- Provisional Sum (2.5% xA)	515,757.51
E	Sub Total (B+C+D)	3,196,699.54
F	TOTAL ESTIMATED COST (A+E)	23,827,000.00
	VAT – 18% of (F)	4,288,860.00
	Grand Total including VAT	**28,115,860.00**

Bill No 02 **REHABILITATION OF DC 01 FROM 0+810 TO 1+189 TRACT 01 LBMC**

OH & PF (without Preliminaries) E * = 16%

Preliminaries P = 4%

SI No	Description	Unit	Qty (A)	Rate (D=B*(1+E))	Amount F=A*D
2.1	Secondary Growth Jungle clearing and removing debries out side the reservation as directed by machinery.	ha	0.30	46,150.00	13,845.00
2.2	Earth excavation and spoil to waste Cut 0-1.5m lift upto 1.5m spread 30m as directed by machinery.	m^3	175.38	365.50	64,101.39
2.3	Supplying, fixing & removing for 600 x 450 x 150mm size polysag sand baging for coffer damming as directed by manually.	Nos	7.00	438.50	3,069.50
2.4	Dealing with water during construction period using 50 mm dia water pump with fuel and operator	Hrs	115.00	942.50	108,387.50
2.5	Supplying & laying polythene 36/500 Gauge (150 g/m^2)	m^2	568.50	188.50	107,162.25
2.6	Mixing, Placing, compaction of Grade 15 Screed concrete (1:3:6) (Grade metal mix 5mm-25mm) including local transports. Lift up to 1.5 m haul 30 m by machinery.	m^3	28.42	36,125.00	1,026,672.50
2.7	Furnishing, transporting, cutting tor steel reinforcement bars (RB500) in to required sizes, bending and binding with binding wires including local transport	Kg	7909.13	526.00	4,160,202.38
2.8	Supplying making & fixing 18 mm thick Ordinary Plywood formworks for each of 6 uses & removing same once including loading and unloading.	m^2	1326.50	3,791.00	5,028,761.50

2.9	Mixing, Placing, compaction of Grade 20 concrete (1:2:4) (Grade metal mix 5mm-20mm) using poker vibrator. Slump shall be less than 150mm and curing shall be done for 28 days. Form work measured separately, including local transports.Lift up to 1.5 m haul 30 m by machinery.	m^3	176.23	40,553.00	7,146,655.19
2.10	Providing construction joint using 25 mm thick regiform sheets at 11.6m intervels as directed.	m^2	14.88	811.00	12,067.68
2.11	Supplying, Tranporting, Placing & copm. Earth in canal using 3T vibrating roller including watering. Cut 0 - 1.5m, lift upto 1.5m, haul 15000m by tractor trailor.	m^3	593.49	3,461.00	2,054,068.89
2.12	Making boundary stones for D Canal reservation path.	Nos	18.00	6,535.00	117,630.00
2.13	Fixing & Installing of Gauge & Current meatering the canals & draw the discharge graphs.	Item	Allow	P.Sum	100,000.00
Bill No 02 Sub Total Cost					19,942,623.78

ESTIMATE OF THE EXPENCE NECESSARY TO BE INCURRED FOR REHABILITATION OF DC 01 FROM 1+320 TO 1+781 TRACT 01 LBMC LUNUGAMWEHERA SCHEME IN TISSAMAHARAMA DIVISION - IRDCRP 2026

SUMMARY OF ESTIMATE

PACKAGE NO :-

Bill No	Description	Amount (LKR)
Bill No 01	Preliminaries(4% of Basic Cost)	497,860.54
Bill No 02	Rehabilitation of DC 01 from 1+320 TO 1+781 Tract 01 LBMC	14,437,955.64
A	Sub Total - Summary of Bills 1 & 2	14,935,816.18
B	Physical Contingencies (Approximately 10% x A)	1,492,713.94
C	Price Contingencies (3% xA)	448,074.49
D	Compliance with Environmental and Social code of Practice (ESCOP)- Provisional Sum (2.5% xA)	373,395.40
E	Sub Total (B+C+D)	2,314,183.83
F	TOTAL ESTIMATED COST (A+E)	17,250,000.00
	VAT – 18% of (F)	3,105,000.00
	Grand Total including VAT	**20,355,000.00**

Bill No 02 **REHABILITATION OF DC 01 FROM 1+320 TO 1+781 TRACT 01 LBMC**

OH & PF (without Preliminaries) E * = 16%

Preliminaries P = 4%

SI No	Description	Unit	Qty (A)	Rate (D=B*(1+E))	Amount F=A*D
2.1	Secondary Growth Jungle clearing and removing debries out side the reservation as directed by machinery.	ha	0.47	46,150.00	21,690.50
2.2	Earth excavation and spoil to waste Cut 0-1.5m lift upto 1.5m spread 30m as directed by machinery.	m^3	78.21	365.50	28,585.76
2.3	Supplying, fixing & removing for 600 x 450 x 150mm size polysag sand baging for coffer damming as directed by manually.	Nos	7.00	409.50	2,866.50
2.4	Dealing with water during construction period using 50 mm dia water pump with fuel and operator	Hrs	60.00	942.50	56,550.00
2.5	Supplying & laying polythene 36/500 Gauge (150 g/m^2)	m^2	410.50	188.50	77,379.25
2.6	Mixing, Placing, compaction of Grade 15 Screed concrete (1:3:6) (Grade metal mix 5mm-25mm) including local transports. Lift up to 1.5 m haul 30 m by machinery.	m^3	20.52	36,125.00	741,285.00
2.7	Furnishing, transporting, cutting tor steel reinforcement bars (RB500) in to required sizes, bending and binding with binding wires including local transport	Kg	5440.42	526.00	2,861,660.92
2.8	Supplying making & fixing 18 mm thick Ordinary Plywood formworks for each of 6 uses & removing same once including loading and unloading.	m^2	1205.53	3,791.00	4,570,164.23

2.9	Mixing, Placing, compaction of Grade 20 concrete (1:2:4) (Grade metal mix 5mm-20mm) using poker vibrator. Slump shall be less than 150mm and curing shall be done for 28 days. Form work measured separately, including local transports.Lift up to 1.5 m haul 30 m by machinery.	m^3	96.83	40,553.00	3,926,746.99
2.10	Providing construction joint using 25 mm thick regiform sheets at 11.6m intervels as directed.	m^2	7.93	811.00	6,431.23
2.11	Supplying, Tranporting, Placing & copm. Earth in canal using 3T vibrating roller including watering. Cut 0 - 1.5m, lift upto 1.5m, haul 15000m by tractor trailor.	m^3	541.66	3,461.00	1,874,685.26
2.12	Making boundary stones for D Canal reservation path.	Nos	26.00	6,535.00	169,910.00
2.13	Fixing & Installing of Gauge & Current meatering the canals & draw the discharge graphs.	Item	Allow	P.Sum	100,000.00
Bill No 02 Sub Total Cost					14,437,955.64
